





|   |  |
|---|--|
|  | <p align="center"><b>ICS Weekly Project Report</b><br/>December 7, 2020</p>  |
|  | <p align="center">ISD #465 Litchfield Public Schools<br/>2019 Referendum</p> |

**District Wide**

- **Completed for Week ending Friday, December 4, 2020**
  - POC meeting was held on 12/02/20

**Lake Ripley Elementary**

- **Completed Week ending Friday, December 4, 2020,**
  - Kitchen/Cafeteria Addition
    - Continued above grade exterior masonry walls
    - New concrete piers and pier corrections
    - Removed terrazzo and concrete flooring for new cleanouts
  - Main Entrance and Office Administration
    - Finished drywall installation
    - Started taping and mudding walls
  - Interior renovations Summer 2021/2022 work
    - Continued execution of contracts with each work scope contractor
    - Scheduled furniture user group kick off meeting for 12/15
- **Planned for Week ending Friday, December 11, 2020**
  - Kitchen/Cafeteria Addition
    - Continue above grade exterior masonry walls
    - Finish new concrete piers
  - Main Entrance and Office Administration
    - Finish taping and mudding walls
    - Start painting
  - Interior renovations Summer 2021/2022 work
    - Executed contracts
    - Continue submittal logs
    - Schedule project kick off meeting

|   |   |
|---|---|
|  | <b>ICS Weekly Project Report</b><br>December 7, 2020  |
|  | ISD #465 Litchfield Public Schools<br>2019 Referendum |

### **Middle School**

- **Completed Week ending Friday, December 4, 2020**
  - Continued to work on construction documents
  - Scheduled furniture user group kick off meeting for 12/15
- **Planned for Week ending Friday, December 11, 2020**
  - Work on bid construction documents

### **High School**

- **Completed Week ending Friday, December 4, 2020**
  - Continued to work on construction documents
  - Scheduled furniture user group kick off meeting for 12/15
  - Scheduled additional user group for FACS to coordinate grant scope
- **Planned for Week ending Friday, December 11, 2020**
  - Work on bid construction documents



ICS Weekly Project Report  
December 7, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley Kitchen Addition Above Grade Masonry Walls Installation





ICS Weekly Project Report  
December 7, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Kitchen Addition Interior Work Terrazzo/Concrete Removal for New Drain Cleanouts**







ICS Weekly Project Report  
December 7, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Main Entrance and Office Administration, Taping, Mudding, Sanding of Drywall and Mechanical and Electrical Rough Ins**





|   |  |
|---|--|
|  | <p align="center"><b>ICS Weekly Project Report</b><br/>December 14, 2020</p> |
|  | <p align="center">ISD #465 Litchfield Public Schools<br/>2019 Referendum</p> |

**District Wide**

- **Planned for Week ending Friday, December 12/18, 2020**
  - POC meeting scheduled for 12/16/20

**Lake Ripley Elementary**

- **Completed Week ending Friday, December 11, 2020,**
  - Kitchen/Cafeteria Addition
    - Continued above grade exterior masonry walls
    - Finished concrete piers and pier corrections
    - Removed old drain clean outs
  - Main Entrance and Office Administration
    - Finished taping and mudding walls
    - Started painting door frames and walls
  - Interior renovations Summer 2021/2022 work
    - Finished execution of contracts
- **Planned for Week ending Friday, December 18, 2020**
  - Kitchen/Cafeteria Addition
    - Continue above grade exterior masonry walls
  - Main Entrance and Office Administration
    - Finish painting
    - Start installation of ceiling grid
  - Interior renovations Summer 2021/2022 work
    - Continue submittal logs
    - Furniture user group kick off meeting scheduled 12/15

|   |   |
|---|---|
|  | <b>ICS Weekly Project Report</b><br>December 14, 2020 |
|  | ISD #465 Litchfield Public Schools<br>2019 Referendum |

### **Middle School**

- **Completed Week ending Friday, December 11, 2020**
  - Continued to work on construction documents
  - Furniture user group kick off meeting scheduled 12/15
- **Planned for Week ending Friday, December 18, 2020**
  - Work on bid construction documents

### **High School**

- **Completed Week ending Friday, December 11, 2020**
  - Continued to work on construction documents
- **Planned for Week ending Friday, December 18, 2020**
  - Furniture user group kick off meeting scheduled 12/15
  - Second user group for FACS scheduled on 12/15
  - Work on bid construction documents



ICS Weekly Project Report  
December 14, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley Kitchen Addition Above Grade Masonry Walls Installation







ICS Weekly Project Report  
December 14, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Kitchen Addition Interior Work Installation of Removal of Old Drain  
Cleanouts**





ICS Weekly Project Report  
December 14, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Main Entrance and Office Administration, Painting of Walls, and Door Frames**







ICS Weekly Project Report  
December 14, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Main Entrance and Office Administration, infill of openings**





|   |  |
|---|--|
|  | <p align="center"><b>ICS Weekly Project Report</b><br/>December 21, 2020</p> |
|  | <p align="center">ISD #465 Litchfield Public Schools<br/>2019 Referendum</p> |

**District Wide**

- **Completed for Week ending Friday, December 18, 2020**
  - ICS provided timeline of project for the new School Board members
  - POC meeting was held for 12/16/20
- **Planned for Week ending Friday, December 25, 2020**
  - Meet on technology responsibility matrix and scope 12/23/20

**Lake Ripley Elementary**

- **Completed Week ending Friday, December 18, 2020,**
  - Kitchen/Cafeteria Addition
    - Continued above grade exterior masonry walls
  - Main Entrance and Office Administration
    - Finished painting
    - Started installation of ceiling grid and pad
    - Started installing lights
    - Installed marker boards
  - Interior renovations Summer 2021/2022 work
    - Continued submittal logs
    - Held furniture user group kick off meeting on 12/15
    - Scheduled project kick off meeting for 1/15/21
- **Planned for Week ending Friday, December 25, 2020**
  - Kitchen/Cafeteria Addition
    - Continue above grade exterior masonry walls
  - Main Entrance and Office Administration
    - Finish installation of ceiling grid
    - Finish installing lights, and mechanical diffusers
    - Abatement
  - Interior renovations Summer 2021/2022 work
    - Continue submittal logs

|   |   |
|---|---|
|  | <b>ICS Weekly Project Report</b><br>December 21, 2020 |
|  | ISD #465 Litchfield Public Schools<br>2019 Referendum |

### **Middle School**

- **Completed Week ending Friday, December 18, 2020**
  - Continued to work on construction documents
  - Furniture user group kick off meeting held on 12/15
- **Planned for Week ending Friday, December 25, 2020**
  - Work on bid construction documents

### **High School**

- **Completed Week ending Friday, December 18, 2020**
  - Continued to work on construction documents
  - Furniture user group kick off meeting held on 12/15
  - Second user group for FACS held on 12/15
- **Planned for Week ending Friday, December 25, 2020**
  - Work on bid construction documents




ICS Weekly Project Report  
December 21, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley Kitchen Addition Above Grade Masonry Walls Installation

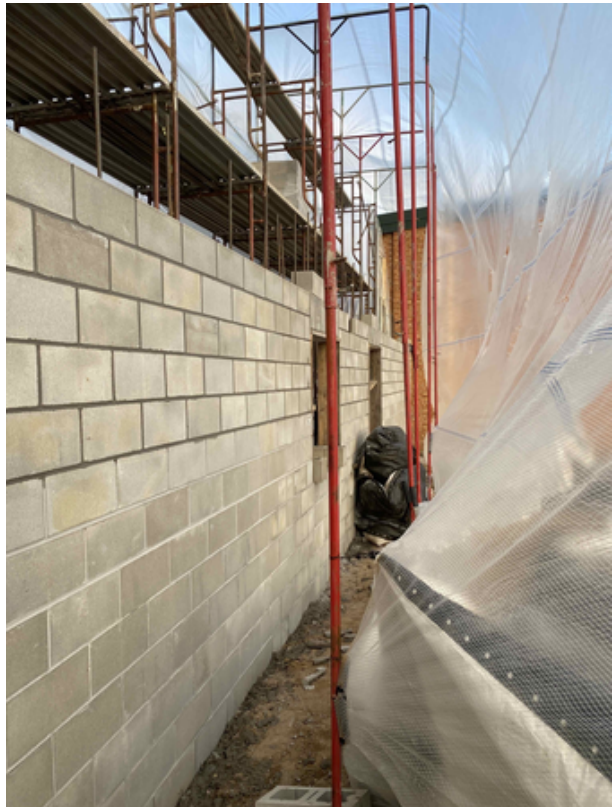



ICS Weekly Project Report  
December 21, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Kitchen Addition Interior Work Pour Back Flooring at Underground  
Sanitary Cleanout Replacement**





ICS Weekly Project Report  
December 21, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Main Entrance and Office Administration Markerboard Installation**









ICS Weekly Project Report  
December 21, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Main Entrance and Office Administration Ceiling Pad and Lights**





|   |  |
|---|--|
|  | <p align="center"><b>ICS Weekly Project Report</b><br/>December 28, 2020</p> |
|  | <p align="center">ISD #465 Litchfield Public Schools<br/>2019 Referendum</p> |

### **District Wide**

- **Completed for Week ending Friday, December 25, 2020**
  - Met on technology responsibility matrix and scope 12/23/20
  - POC meeting was held for 12/16/20
- **Planned for Week ending Friday, January 1, 2020**
  - POC meeting was scheduled for 12/30/20

### **Lake Ripley Elementary**

- **Completed Week ending Friday, December 25, 2020,**
  - Kitchen/Cafeteria Addition
    - Continued above grade exterior masonry walls
  - Main Entrance and Office Administration
    - Finished installation of ceiling grid
    - Finished installing lights, and mechanical diffusers
    - Abatement
    - Floor leveling and preparation for carpet
  - Interior renovations Summer 2021/2022 work
    - Continued submittal logs
- **Planned for Week ending Friday, January 1, 2020**
  - Kitchen/Cafeteria Addition
    - Continue above grade exterior masonry walls
    - Start setting structural steel
  - Main Entrance and Office Administration
    - Begin millwork installation
    - Install HVAC diffusers and return grills
    - Start flooring
  - Interior renovations Summer 2021/2022 work
    - Review mechanical equipment submittals and shop drawings

|   |   |
|---|---|
|  | <b>ICS Weekly Project Report</b><br>December 28, 2020 |
|  | ISD #465 Litchfield Public Schools<br>2019 Referendum |

### **Middle School**

- **Completed Week ending Friday, December 25, 2020**
  - Continued to work on construction documents
- **Planned for Week ending Friday, January 1, 2020**
  - Work on bid construction documents
  - Work on cost estimates

### **High School**

- **Completed Week ending Friday, December 25, 2020**
  - Continued to work on construction documents
- **Planned for Week ending Friday, January 1, 2020**
  - Work on bid construction documents
  - Work on cost estimates



ICS Weekly Project Report  
December 28, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Kitchen Addition Above Grade Masonry Walls Installation**





ICS Weekly Project Report  
December 28, 2020



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley Main Entrance and Office Administration Floor Leveling and Millwork Installation**

