


	<p align="center">ICS Weekly Project Report April 05, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, April 2, 2021**
- **Planned for Week ending Friday, April 9, 2021**
 - Furniture oversight group meeting scheduled for 04/05/21
 - POC meeting scheduled for 04/07/21

Lake Ripley Elementary

- **Completed Week/ ending Friday, April 2, 2021**
 - Kitchen/Cafeteria Addition
 - Continued installing ceiling grid
 - Continued installing wall tile
 - Touched up mudding, taping of soffits/walls
 - Touched up paint
 - Installation of floor tile
 - Started installation of handwashing stations
 - Main Entrance and Office Administration
 - Testing, balancing, and commissioning of HVAC system
 - Interior renovations Summer 2021/2022 work
 - Continued reviewing and approving shop drawings
 - Abatement in old administration offices
 - Construction meeting was held on 4/2/21
- **Planned for Week ending Friday, April 9, 2021**
 - Kitchen/Cafeteria Addition
 - Finish hand washing station installation
 - Start exterior panel installation
 - Start exterior dirt work
 - Finish ceiling grid
 - Finish wall and floor tile
 - Start installing mechanical diffusers in ceilings
 - Interior renovations Summer 2021/2022 work
 - Continue reviewing and approving shop drawings
 - Demolition in old administration offices

	<p>ICS Weekly Project Report April 05, 2021</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle School/High School

- **Completed Week ending Friday, April 2, 2021**
 - Build detail schedule
 - Review and approve shop drawings
 - Abatement in auditorium and two art classrooms
- **Planned for Week ending Friday, April 9, 2021**
 - Build detail schedule
 - Review and approve shop drawings
 - Finish abatement in auditorium



ICS Weekly Project Report
April 05, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition – Tiling of Floors






ICS Weekly Project Report
April 05, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Had Washing/Drying Stations

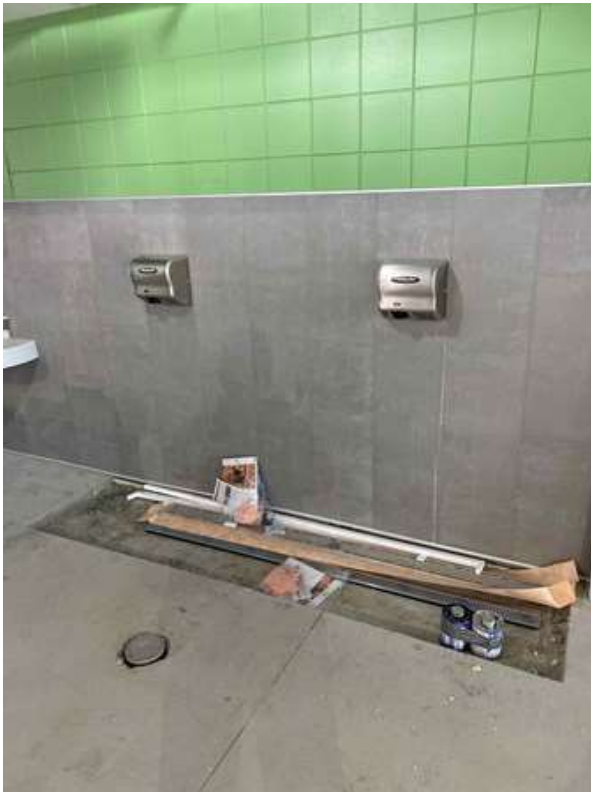



ICS Weekly Project Report
April 05, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Interior Renovations – Demolition of Old Administration Offices





ICS Weekly Project Report
April 05, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School Interior Renovations – Art Classroom Abatement







ICS Weekly Project Report
April 05, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School Interior Renovations – Auditorium Abatement





	<p align="center">ICS Weekly Project Report April 12, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, April 9, 2021**
 - Furniture oversight group meeting was held on 04/05/21
 - POC meeting was held on 04/07/21
- **Planned for Week ending Friday, April 16, 2021**

Lake Ripley Elementary

- **Completed Week/ ending Friday, April 9, 2021**
 - Kitchen/Cafeteria Addition
 - Finished hand washing station installation
 - Started exterior panel installation
 - Started exterior dirt work
 - Finished wall and floor tile
 - Started installing mechanical diffusers in ceilings
 - Started installing Fiber reinforced plastic (FRP) wall finishes
 - Interior renovations Summer 2021/2022 work
 - Continued reviewing and approving shop drawings
 - Demolition in old administration offices
- **Planned for Week ending Friday, April 16, 2021**
 - Kitchen/Cafeteria Addition
 - Continue exterior panel installation
 - Continue exterior dirt work
 - Continue installing mechanical diffusers in ceilings
 - Continue installing Fiber reinforced plastic (FRP) wall finishes
 - Start installing kitchen equipment
 - Start installing flooring
 - Interior renovations Summer 2021/2022 work
 - Continue reviewing and approving shop drawings
 - Demolition in old administration offices to continue

	ICS Weekly Project Report April 12, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle School/High School

- **Completed Week ending Friday, April 9, 2021**
 - Build detail schedule
 - Review and approve shop drawings
 - Finished abatement in auditorium
- **Planned for Week ending Friday, April 16, 2021**
 - Build detail schedule
 - Review and approve shop drawings
 - Schedule project kick off meeting with contractors




ICS Weekly Project Report
April 12, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition – Tiling Bathroom and Walls

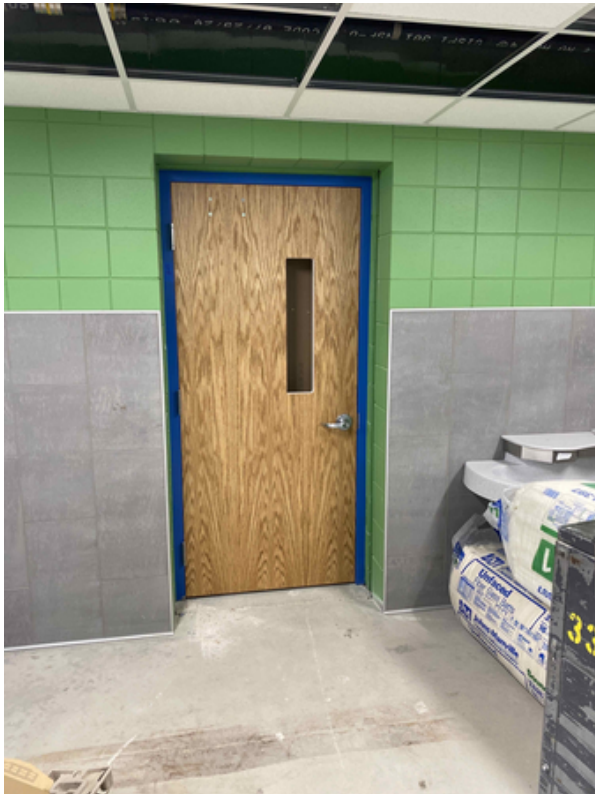



ICS Weekly Project Report
April 12, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

**Lake Ripley Kitchen Addition Doors and Fiber Reinforced Plastic (FRP) Wall
Installation**





ICS Weekly Project Report
April 12, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Interior Renovations – Demolition of Old Administration Offices








ICS Weekly Project Report
April 12, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

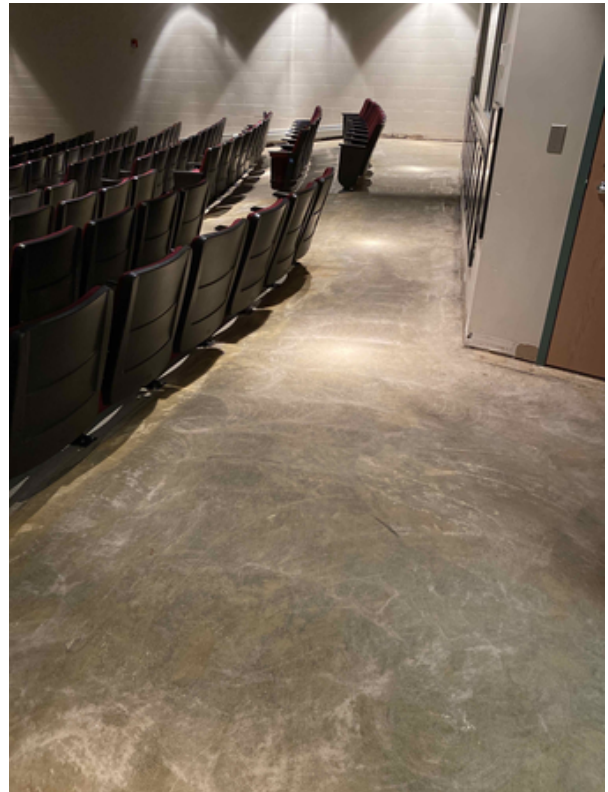High School Interior Renovations – Auditorium Abatement Completed





	<p align="center">ICS Weekly Project Report April 19, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, April 16, 2021**
- **Planned for Week ending Friday, April 23, 2021**
 - POC meeting scheduled for 4/21/21

Lake Ripley Elementary

- **Completed Week/ ending Friday, April 16, 2021**
 - Kitchen/Cafeteria Addition
 - Continued exterior panel installation
 - Continued exterior dirt work
 - Continued installing mechanical diffusers in ceilings
 - Continued installing Fiber reinforced plastic (FRP) wall finishes
 - Started installing kitchen equipment
 - Low voltage installation for card readers and cameras
 - Interior renovations Summer 2021/2022 work
 - Continue reviewing and approving shop drawings
 - Demolition in old administration offices completed
 - Construction coordination meeting held on 4/17/21
- **Planned for Week ending Friday, April 23, 2021**
 - Kitchen/Cafeteria Addition
 - Continue exterior panel installation
 - Finish installing kitchen equipment
 - Start exterior concrete door stoops
 - Install coiling doors
 - Continue mechanical and electrical terminations and finishes
 - Interior renovations Summer 2021/2022 work
 - Continue reviewing and approving shop drawings
 - Pour back concrete flooring patches
 - Wall framing to start

	ICS Weekly Project Report April 19, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle School/High School

- **Completed Week ending Friday, April 16, 2021**
 - Build detail schedule
 - Review and approve shop drawings
- **Planned for Week ending Friday, April 23, 2021**
 - Review and approve shop drawings
 - Project kick off meeting with contractors scheduled for 4/22/21



ICS Weekly Project Report
April 19, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition – Exterior Panel Installation





ICS Weekly Project Report
April 19, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Exterior Dirt Work and Grading





ICS Weekly Project Report
April 19, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Ceiling Complete and Kitchen Equipment Installation





ICS Weekly Project Report



April 19, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Interior Renovations – Demolition of Old Administration Offices Complete and Preparation for Pouring Back Concrete Floors





	<p align="center">ICS Weekly Project Report April 26, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, April 23, 2021**
 - POC meeting was held on 4/21/21
- **Planned for Week ending Friday, April 30, 2021**
 - Meeting with Administration to discuss Media Center move in/out logistics 4/30/21

Lake Ripley Elementary

- **Completed Week/ ending Friday, April 23, 2021**
 - Kitchen/Cafeteria Addition
 - Continued exterior panel installation
 - Installation kitchen equipment
 - Started exterior concrete door stoops
 - Started installation coiling doors
 - Continued mechanical and electrical terminations and finishes
 - Exterior grading, excavation, and sanitary piping installation
 - Interior renovations Summer 2021/2022 work
 - Continued reviewing and approving shop drawings
 - Poured back concrete flooring patches
 - Started wall and door framing
- **Planned for Week ending Friday, April 30, 2021**
 - Kitchen/Cafeteria Addition
 - Finish exterior panel installation
 - Finish mechanical and electrical terminations and finishes
 - Finish installation of kitchen equipment
 - Finish exterior concrete work
 - Finish installation of coiling doors
 - Finish exterior dirt work and grading
 - Interior renovations Summer 2021/2022 work
 - Continue reviewing and approving shop drawings
 - Rough in plumbing within wall framing
 - Rough in electrical conduits
 - Construction coordination meeting with contractors scheduled for 4/29/21

	ICS Weekly Project Report April 26, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle School/High School

- **Completed Week ending Friday, April 23, 2021**
 - Build detail schedule
 - Review and approve shop drawings
 - Project kick off meeting with contractors was held on 4/22/21
- **Planned for Week ending Friday, April 30, 2021**
 - Review and approve shop drawings
 - ICS finalizing critical path method (CPM) construction schedule



ICS Weekly Project Report
April 26, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition – Exterior Panel Installation





ICS Weekly Project Report
April 26, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Exterior Dirt Work and Sanitary Line Installation





ICS Weekly Project Report
April 26, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Kitchen Equipment Installation





ICS Weekly Project Report
April 26, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

**Lake Ripley Interior Renovations – Demolition of Old Administration Offices/New
Special Education Suite**

