


	<p align="center">ICS Weekly Project Report August 2, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Planned for Week ending Friday, August 6, 2021**
 - POC meeting scheduled for 08/04/21

Lake Ripley Elementary

- **Completed Week ending Friday, July 30, 2021**
 - Interior renovations Summer 2021/2022 work
 - Continued sprinkler work, ceiling grid, light fixtures, and diffusers in corridors
 - Sprinkler work, and padded out classroom ceilings
 - Media Center, STEAM, Speech classroom offices drywall and wall tile
 - Installation of ceiling grid, light fixtures, toilets, and sprinkler work in bathrooms
 - Paint walls, door frames in special education suite
 - Installed ceiling grid, sprinkler work, diffusers, lights and markerboards in special education suite
 - Framed walls in staff collaboration space
 - Continued mechanical and electrical rough ins for staff collaboration space
 - Started installing new mechanical units on mezzanine level
 - Joist pockets in gymnasium and old cafeteria for steel joists
- **Planned for Week ending Friday, August 6, 2021**
 - Interior renovations Summer 2021/2022 work
 - Gymnasium duct removal
 - Continue sprinkler work, ceiling grid, light fixtures, and diffusers in corridors
 - Finish drywall and paint in Media Center, STEAM, Speech classroom offices
 - Install ceiling grid and glass doors in Media Center, STEAM, Speech classroom offices
 - Finish ceilings and remove floor protection in classrooms for floor waxing
 - Install toilet partitions and lights in bathrooms
 - Install ceiling pad, paint door frames, and install flooring in Special Education Suite
 - Install ductwork and in wall mechanical electrical rough ins for staff collaboration space

	<p align="center">ICS Weekly Project Report August 2, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle School/High School

- **Completed Week/ ending Friday, July 30, 2021**
 - Middle School
 - Completed all in-wall plumbing and electrical rough-in.
 - Continued insulating plumbing and mechanical lines.
 - Continued acoustical ceiling grid installation.
 - Began installing mechanical and electrical ceiling finishes.
 - Continued drywall hanging and taping.
 - Continued painting.
 - Started installing casework.
 - High School
 - Completed structural steel erection in the Admin. area.
 - Completed concrete slab infills throughout.
 - Completed concrete footings and foundation walls for concrete ramps and stairs in the commons area.
 - Continued framing metal stud partitions.
 - Completed in-wall plumbing rough-in.
 - Continued insulating plumbing and mechanical lines.
- **Planned for Week ending Friday, August 6, 2021**
 - Middle School
 - Continue drywall hanging and taping, sanding drywall.
 - Continue painting.
 - Continue acoustical ceiling grid installation and begin installing ceiling tiles.
 - Continue installing mechanical and electrical ceiling finishes.
 - Continue insulating overhead plumbing and mechanical systems.
 - Begin tile work in the Locker Room and Toilet Room areas.
 - Continue installing casework.
 - Begin installing plumbing fixtures.
 - High School
 - Complete slab prep and upper concrete (corridor) slabs in the Commons areas.
 - Continue electrical rough-in in the Admin. and Special Ed. spaces.



ICS Weekly Project Report

August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

- Complete in-wall electrical rough-in.
- Continue insulating plumbing and mechanical lines.
- Continue hanging and taping drywall.
- Complete last remaining structural steel erection in the corridors.



ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Classrooms Finished Minus New Casework - Floors Cleaned Waxed






ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Staff Collaboration Space Wall Framing

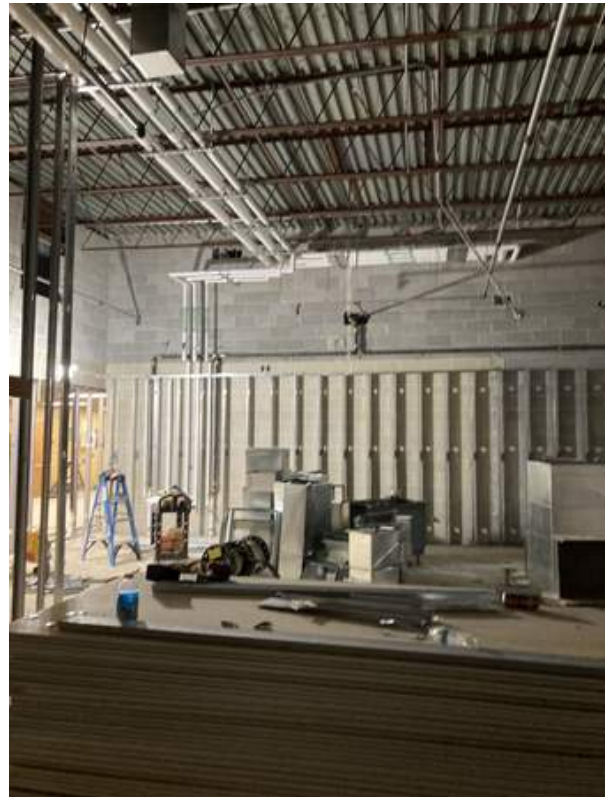



ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Large Bathrooms





ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Media Center Entrance Wall Tile and Soffit Framing





ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Special Ed. Suite Walls Painted, Ceiling Grid and Markerboards Installed





ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Special Ed. area door frames installed and drywall hang, tape and finish in-progress. Reception area desk framing.






ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Art Room and FACS Lab progress.

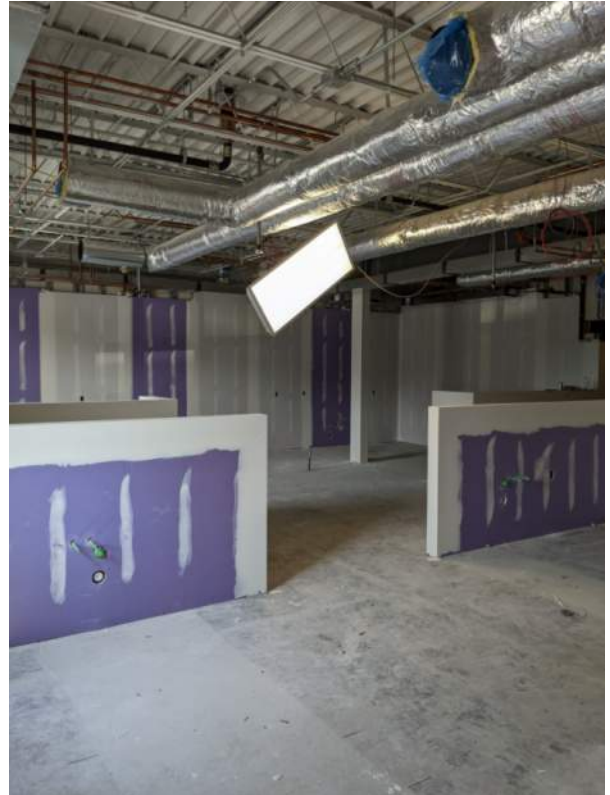




ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons area progress.

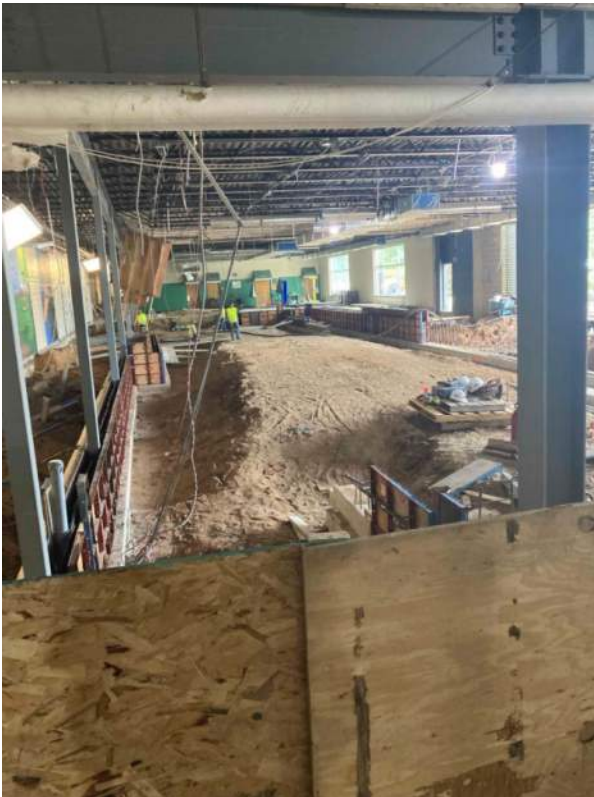





ICS Weekly Project Report
August 2, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Admin area drywall installation. Special Ed. area metal stud framing and in-wall rough-in.





	<p align="center">ICS Weekly Project Report August 9, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed Week ending Friday, August 6, 2021**
 - POC meeting was held on 08/04/21

Lake Ripley Elementary

- **Completed Week ending Friday, August 6, 2021**
 - Kitchen
 - Electrical modifications for Servery and other kitchen equipment
 - Interior renovations Summer 2021/2022 work
 - Continued sprinkler work, ceiling grid, light fixtures, and diffusers in corridors
 - Sprinkler work, and padded out classroom ceilings
 - Finished drywall and started paint in Media Center, STEAM, Speech classroom offices
 - Finished ceilings and remove floor protection in classrooms for floor waxing
 - Installed toilet partitions and lights in bathrooms
 - Installed ceiling pad, paint door frames, and install flooring in Special Education Suite
 - Installed ductwork and in wall mechanical electrical rough ins for staff collaboration space
 - Drywall work in staff collaboration space
 - Gymnasium duct removal
 - Set mechanical rooftop units on roof via crane
- **Planned for Week ending Friday, August 13, 2021**
 - Interior renovations Summer 2021/2022 work
 - Steel joist installation in gymnasium and old cafeteria/new multipurpose room
 - Install ceiling grid glass doors, finish drywall and paint in Media Center, STEAM, Speech classroom offices
 - Ceiling grid and light fixtures in STEAM, and Speech classrooms and offices
 - Piping, and HVAC ductwork for mechanical and mezzanine rooftop units
 - Finish ceiling pad and start punch list in bathrooms
 - Paint walls, install carpet, and doors in Special Education Suite
 - Start installing ceiling pad throughout

	<p align="center">ICS Weekly Project Report August 9, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle School/High School

- **Completed Week/ ending Friday, August 6, 2021**
 - Middle School
 - Began acoustical ceiling tile in the corridors.
 - Continued hanging and taping drywall in the Special Ed. area.
 - Continued painting throughout.
 - Continued acoustical ceiling grid installation in the classrooms and offices.
 - Continued installing lights, diffusers and grilles in the ceilings.
 - Continued installing casework.
 - Continue insulating plumbing and mechanical lines.
 - High School
 - Completed the upper concrete slabs (corridors) in the Commons area.
 - Completed drywall taping and sanding in the Admin. area.
 - Continued in-wall rough-in in the Special Ed. area.
 - Continued hydronic and plumbing mains in the Commons area.
 - Continue insulating plumbing and mechanical lines.
- **Planned for Week ending Friday, August 13, 2021**
 - Middle School
 - Begin installing vinyl tile flooring.
 - Continue casework installation.
 - Begin tile work in the Locker Room and Toilet rooms.
 - Continue painting throughout.
 - Continue installing plumbing fixtures.
 - Continue installing lights, diffusers and grilles.
 - Continue installing acoustical ceiling tiles throughout.
 - High School
 - Continued hydronic and plumbing mains in the Commons area.
 - Complete all remaining concrete in the Commons area.
 - Complete last remaining structural steel erection in the corridors.
 - Complete drywall hanging and taping in the Special Ed. area.
 - Begin painting in the Special Ed. and Admin areas.
 - Begin acoustical ceiling grid installation in the Admin. area.



ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Mechanical Roof Top Units Craned and Set





ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Staff Collaboration Drywall





ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Large Bathrooms Toilet Partitions Installed






ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Media Center Entrance Drywall and Painting

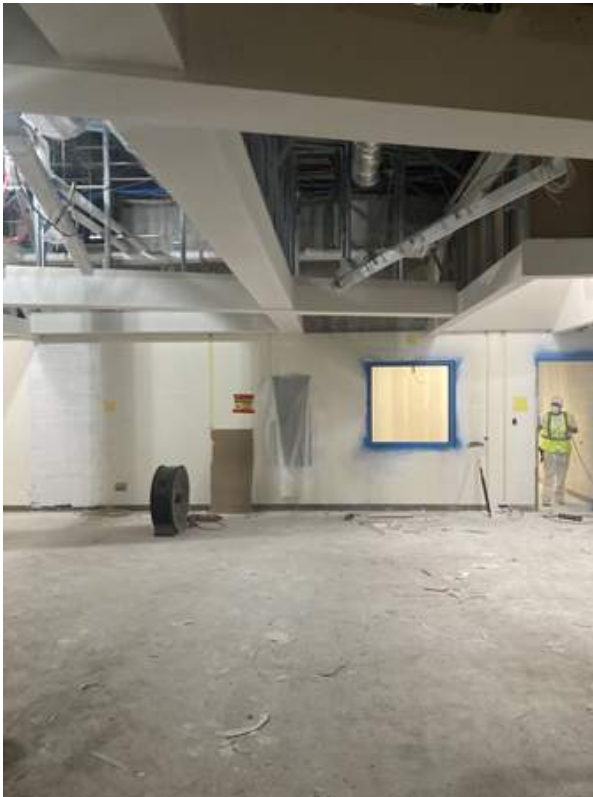



ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Special Ed. Suite Carpet Installation





ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Corridor Painting, Ceiling and Light Fixture Progress





ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Casework installation in the FACS Lab and Classrooms.





ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Ceiling tile installation in the corridors. Painting in the Special Ed. Area.





ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Sound insulation in the walls and drywall installed in the Special Ed. area.







ICS Weekly Project Report
August 9, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Concrete ramps poured in the Commons area. Drywall taped and sanded in the Admin. area.



	<p align="center">ICS Weekly Project Report August 16, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary

- **Completed Week ending Friday, August 13, 2021**



Interior renovations Summer 2021/2022 work

- Steel joist installation in gymnasium
- Installed ceiling grid glass doors, finish drywall and paint in Media Center, Speech classroom offices
- Ceiling grid and light fixtures in, and Speech classrooms and offices
- Piping, and HVAC ductwork for mechanical and mezzanine rooftop units
- Painted walls, install carpet, and door frames in Special Education Suite
- Started installing ceiling pad throughout
- Grout wall tile at Breakout space and Media Center entrance
- Wall and floor tile in staff bathroom next to staff collaboration space
- Painted staff collaboration room
- Started installing new exterior doors

- **Planned for Week ending Friday, August 20, 2021**

Interior renovations Summer 2021/2022 work

- Finish sprinkler work, ceiling pads, and paint touch up throughout
- Furniture delivery and installation
- Steel joist installation in old cafeteria/new multipurpose room
- Ductwork installation, and paint in gymnasium
- Install interior windows-glazing in Media Center-STEAM and Speech Offices
- Finish ceilings, light fixtures and diffusers in Media Center-STEAM and Speech
- Floor base installation in Special Education Suite.
- Floor prep work in Staff Collaboration and Privacy Room (Mothers Room)
- Start installing casework and sinks in classrooms
- Finish piping and ductwork to new HVAC units
- Startup mechanical equipment and units 8/19
- Finish installing new exterior doors
- Final alarm and life safety testing scheduled for 8/20
- Remove floor protection
- Punchlist and start cleaning

	<p align="center">ICS Weekly Project Report August 16, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle School/High School

- **Completed Week/ ending Friday, August 13, 2021**

Middle School

- Continued installing casework. Began installing plastic laminate countertops.
- Began installing plumbing fixtures in countertops.
- Continued painting walls and door frames.
- Completed acoustical ceiling grid installation and nearing completion on acoustical tile installation.
- Began installing vinyl tile flooring.

High School

- Completed drywall finishing and painting in the Admin. area.
- Began installing acoustical ceiling grid in the Admin. area.
- Began installing lights diffusers and grilles in the Admin. area.
- Completed hanging drywall and began taping in the Special Ed. suite.
- Placed the remaining concrete slabs in the Commons area.
- Began installing acoustical ceiling grid in the Admin. area.
- Continued plumbing and hydronic main piping to the main mechanical chase into the tunnel area.

- **Planned for Week ending Friday, August 20, 2021**

Middle School

- Complete casework installation.
- Begin installing solid surface countertops.
- Complete plumbing fixtures in countertops.
- Complete vinyl tile flooring and begin floor prep and carpet tile installation.
- Begin final cleaning.
- Begin assembling and installing new furniture.
- Partial final inspections to allow staff to begin moving into new spaces.

High School

- Complete drywall taping and sanding in the Special Ed. suite.
- Complete painting walls in the Special Ed. Suite.
- Complete acoustical ceiling grid installation in the Special Ed. suite.
- Begin lights, diffusers and grilles in the Special Ed. suite.



ICS Weekly Project Report

August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

- Complete remaining steel required for new rooftop mechanical units.
- Set all rooftop mechanical equipment and complete final mechanical and electrical connections.
- Complete vinyl tile flooring and begin floor prep and carpet tile installation.
- Begin final cleaning.
- Begin assembling and installing new furniture.
- Partial final inspections to allow staff to begin moving into new spaces.



ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Special Education Suite Furniture Delivery and Installation





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Staff Collaboration and Staff Bathroom Paint and Tile Work





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Media Center Entrance and Breakout Areas Wall Tile Grout





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Media Center and Classroom Ceiling Grid





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – New Mezzanine Mechanical Unit and Equipment Connections





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Exterior Door Replacement





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Special Ed. walls painted, ceilings and casework installed.





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Art Room and FACS Lab progress.





ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Special Ed. suite drywall installed, taping and sanding in-progress.









ICS Weekly Project Report
August 16, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

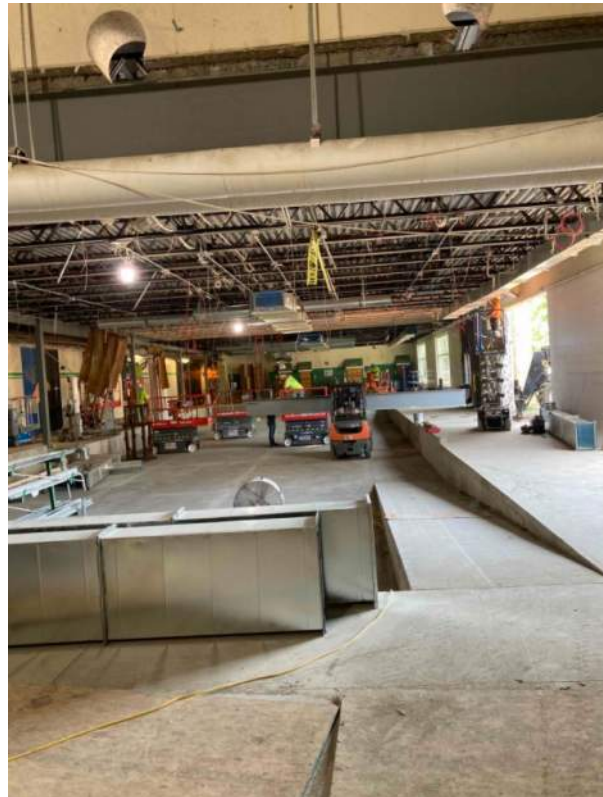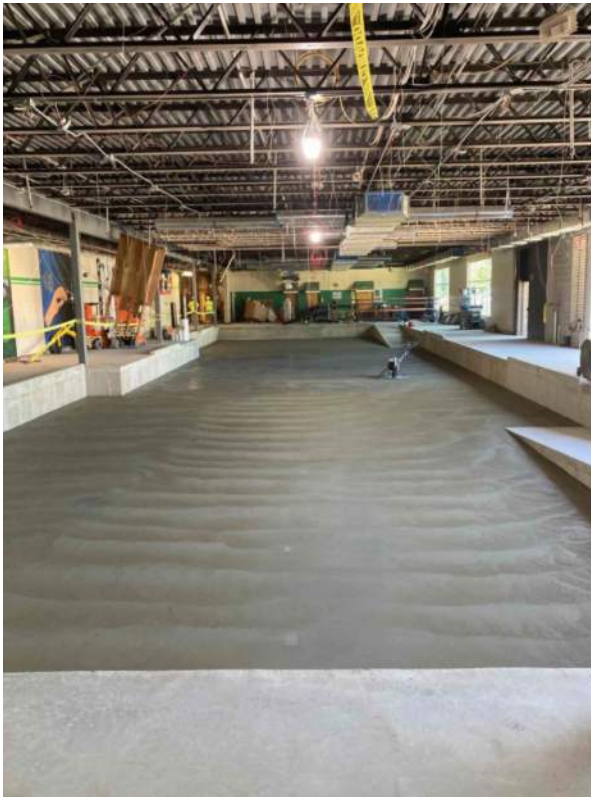High School – Commons area concrete slabs, ramps and stairs completed.





	<p align="center">ICS Weekly Project Report August 23, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary



- **Completed Week ending Friday, August 20, 2021**
 - Interior renovations Summer 2021/2022 work
 - Finished sprinkler work, ceiling pads, and paint touch up throughout
 - Furniture delivery and installation
 - Finish ceiling grid, light fixtures and diffusers in Media Center-STEAM and Speech
 - Carpet in the Media Center
 - Floor prep work in Staff Collaboration and Privacy Room (Mothers Room)
 - Started installing casework and sinks in classrooms
 - Finished piping and to new HVAC units
 - Finish installing new exterior doors
 - Final alarm and life safety testing held and passed on 8/20
 - Removed floor protection
 - Punchlist and started cleaning

- **Planned for Week ending Friday, August 27, 2021**
 - Interior renovations Summer 2021/2022 work
 - Finish ceiling pad, in Media Center-STEAM and Speech
 - Startup mechanical equipment and units
 - Vinyl base installation throughout
 - Ductwork installation, and paint in gymnasium
 - Steel joist installation in old cafeteria/new multipurpose room
 - Install casework and plumbing in classrooms
 - Install glass throughout and sliding doors
 - Start installing ceiling grid in staff collaboration, staff bathroom/privacy room
 - Clearing out south half of gymnasium for use
 - Final testing and inspections scheduled for 8/26
 - Final cleaning

	<p align="center">ICS Weekly Project Report August 23, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle School/High School

- **Completed Week/ ending Friday, August 20, 2021**
 - Middle School
 - Continued installing casework. Began installing solid surface tops.
 - Continued installing plumbing fixtures in countertops.
 - Continued painting walls and door frames.
 - Completed acoustical ceiling tile installation.
 - Continued installing vinyl tile flooring. Began installing carpet tile flooring.
 - Began installing hollow metal doors.
 - Began assembling and installing new furniture.
 - Completed fire alarm testing and inspection.
 - Passed inspection for staff occupancy.
 - High School
 - Completed demolition of the existing electrical main switchboard. Completed the energization of the new main electrical main switchboard.
 - Completed structural steel supports for the rooftop unit serving the Admin. space.
 - Completed plumbing main tie-ins.
 - Completed drywall taping and sanding in the Special Ed. suite.
 - Completed wall painting in the Special Ed. Suite.
 - Began installing lights, grilles and diffusers in the Special Ed. Suite.
 - Continued acoustical ceiling grid installation in the Special Ed. suite.
 - Continued casework installation in the Admin. space and Special Ed. suite.
 - Completed soffit framing and drywall installation in the Main Entrance/Lobby.
- **Planned for Week ending Friday, August 27, 2021**
 - Middle School
 - Continue installing vinyl and carpet tile flooring.
 - Continue installing doors and hardware.
 - Begin final cleaning.
 - Continue furniture assembly and installation.
 - Begin staff move-in.
 - Final inspection for Certificate of Occupancy.

	ICS Weekly Project Report August 23, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

- High School
 - Complete structural steel supports for rooftop mechanical units serving the Special Ed. suite.
 - Hoist and set new rooftop mechanical units and complete final mechanical and electrical connections.
 - Complete lights, diffusers and grilles in the Special Ed. suite.
 - Complete ceiling tile installation in the Special Ed. suite.
 - Complete flooring in the instructional spaces.
 - Complete acoustical ceiling grid in the Main Entrance/Lobby.
 - Begin final cleaning.
 - Begin Staff move-in.
 - Final inspection for Certificate of Occupancy.



ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Classroom Casework and Locker Installation





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Media Center/Classroom Book Shelves and Carpet Installed





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Breakout Areas Carpet and Markerboards Installed





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Staff Collaboration





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – STEAM Room and Media Flex Classroom





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Art Room casework complete.





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – FACS Lab casework completed.





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Classrooms nearing completion, new furniture installed.





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Special Ed. suite classrooms casework.





ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Main Entrance/Lobby soffits.







ICS Weekly Project Report
August 23, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Special Ed. structural steel and operable partition wall in-progress.





	<p align="center">ICS Weekly Project Report August 30, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary

- **Completed Week ending Friday, August 27, 2021**
 - Interior renovations Summer 2021/2022 work
 - Finished ceiling pad, in Media Center-STEAM and Speech
 - Started up mechanical equipment and units
 - Vinyl base and floor installation throughout
 - Ductwork installation, and paint in gymnasium
 - Steel joist installation in old cafeteria/new multipurpose room
 - Installed casework and plumbing in classrooms
 - Installed glass throughout and sliding doors
 - Finished installing lights in gymnasium
 - Clearing out south half of gymnasium for use
 - Final testing and inspections held on 8/26
 - Final cleaning

- **Planned for Week ending Friday, September 3, 2021**
 - Interior renovations Summer 2021/2022 work
 - Start installing ceiling grid in staff collaboration, staff bathroom/privacy room
 - Overhead piping and HVAC ductwork insulation in staff collaboration room
 - Controls and condensing unit installation of HVAC system
 - Install casework in staff collaboration room
 - Vinyl floor and base patching
 - Clear out south half of gymnasium and clean for use
 - Finish sinks in classrooms
 - Finish lockers in corridors
 - Punch list and final cleaning

	<p align="center">ICS Weekly Project Report August 30, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle School/High School

- **Completed Week/ ending Friday, August 27, 2021**
 - Middle School
 - Continued door hardware installation.
 - Continued flooring installation.
 - Completed final cleaning of the renovated spaces.
 - Completed assembling and installing new furniture received to date.
 - Completed staff move-in
 - Passed final inspection for student occupancy.
 - High School
 - Completed structural steel supports for rooftop mechanical units serving the Special Ed. suite.
 - Hoisted and set new rooftop mechanical units and complete final mechanical and electrical connections.
 - Completed lights, diffusers and grilles in the Special Ed. suite.
 - Completed ceiling tile installation in the Special Ed. suite.
 - Completed flooring in the instructional spaces.
 - Completed acoustical ceiling grid in the Main Entrance/Lobby.
 - Completed final cleaning of the renovated spaces.
 - Completed assembling and installing new furniture received to date.
 - Completed staff move-in
 - Passed final inspection for student occupancy.
- **Planned for Week ending Friday, September 3, 2021**
 - Middle School
 - Finish wall base.
 - Complete flooring installation.
 - Begin tile work in the Special Ed. toilet room.
 - Continue installing door hardware.
 - Complete aluminum storefront entrances at the Main Entry/Admin Space.
 - Begin installing glass in door frames.
 - Conduct architectural punchlist walkthrough.
 - High School



ICS Weekly Project Report

August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

- Complete curb framing and roof patching at rooftop units.
- Begin tile work in the Special Ed. toilet room.
- Begin terrazzo patching.
- Begin installing glass in doors and frames.
- Complete floor prep for Admin. area carpet and LVT, begin installing flooring.
- Continue Admin./Reception countertops and p-lam finishes.
- Complete aluminum storefront entrances at the Main Entry/Admin Space.
- Continue miscellaneous painting throughout.
- Continue wall and soffit framing in the Commons.
- Inspection for student and staff occupancy of the Admin. space.



ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Lockers and Vinyl Flooring Patching in Corridors





ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Staff Collaboration Space





ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – New Gymnasium Lights and Ductwork





ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Glass Installed in STEAM Classroom and Media Center Flex Classroom






ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Art and STEM classrooms.

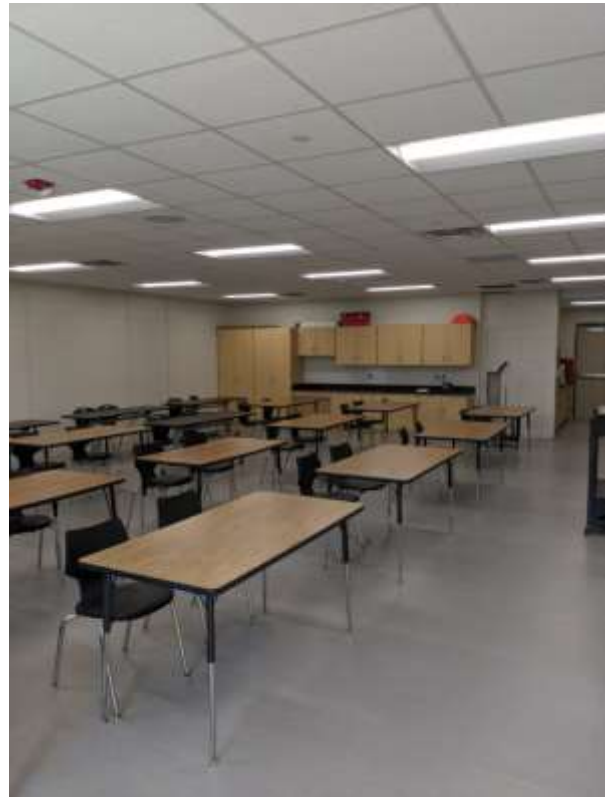



ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – FACS Lab and FACS classroom.





ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Special Ed. Classrooms.






ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – North Commons/Main Entrance and South Commons

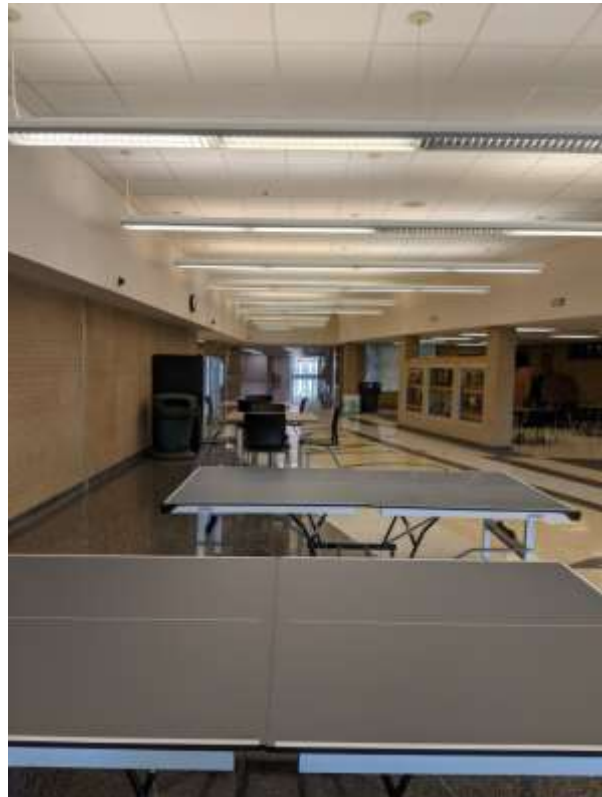




ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Special Ed. classrooms.

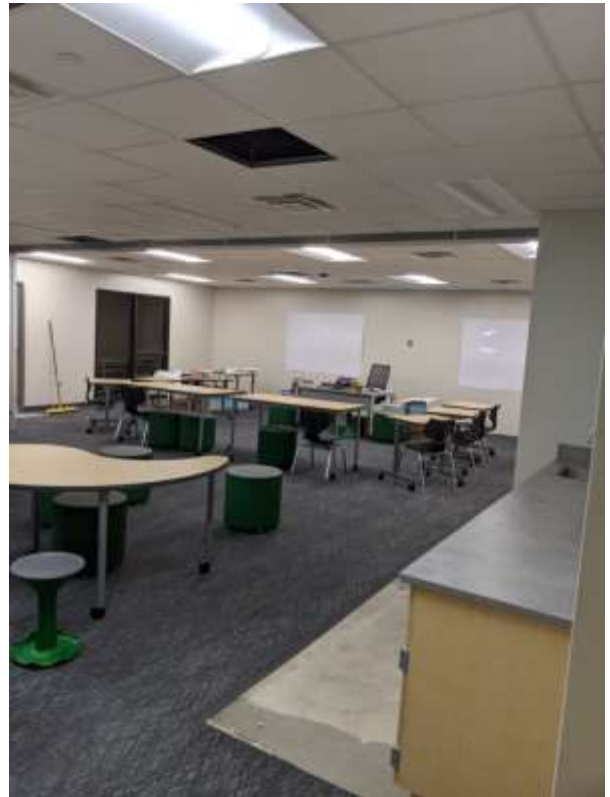



ICS Weekly Project Report
August 30, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Reception and Admin Circulation.

