


	<p align="center"><b>ICS Weekly Project Report</b> December 6, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, December 3, 2021**
  - Continued punch list and commissioning items
- **Planned for Week ending Friday, December 10, 2021**
  - Continue punch list and commissioning items
  - Additional lockers to be delivered

### **Middle School/High School Interior Renovations**

- **Completed Week/ ending Friday, December 3, 2021**
  - Middle School
    - Media Center – Completed above ceiling inspections.
    - Media Center – Completed acoustical ceiling tiles.
    - Media Center – Started wall tile.
    - Continued student locker installation in the corridors.
    - Continued addressing punch list and commissioning items.
  - High School
    - Commons – Completed wall tile.
    - Commons – Completed acoustical wall panels.
    - Commons – Completed bench cushions.
    - Continued addressing punchlist and commissioning items.
- **Planned for Week ending Friday, December 10, 2021**
  - Middle School
    - Media Center – Complete wall tile.
    - Restrooms – Begin floor and wall tile.
    - Continue student locker installation in the corridors.
    - Continue addressing punch list and commissioning items.
  - High School
    - Continue addressing punch list and commissioning items.

	<p><b>ICS Weekly Project Report</b> December 6, 2021</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Middle/High School Parking Lot**

- **Planned for Week ending Friday, December 3, 2021**
  - Continued to work on bid documents.
- **Planned for Week ending Friday, December 10, 2021**
  - Continue to work on bid documents.




**ICS Weekly Project Report**  
December 6, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Ceilings and wall tile.**

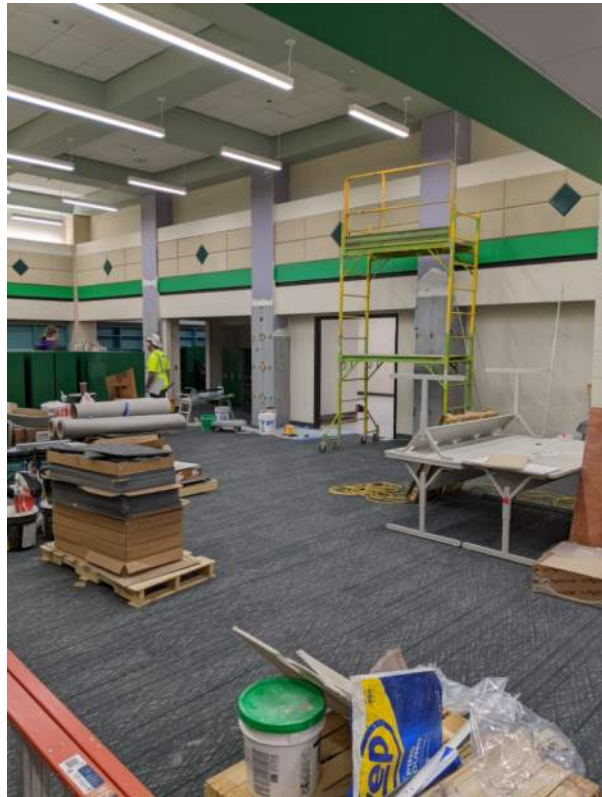



**ICS Weekly Project Report**  
December 6, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Student lockers.**





**ICS Weekly Project Report**  
December 6, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Commons – bench cushions.**








**ICS Weekly Project Report**  
December 6, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

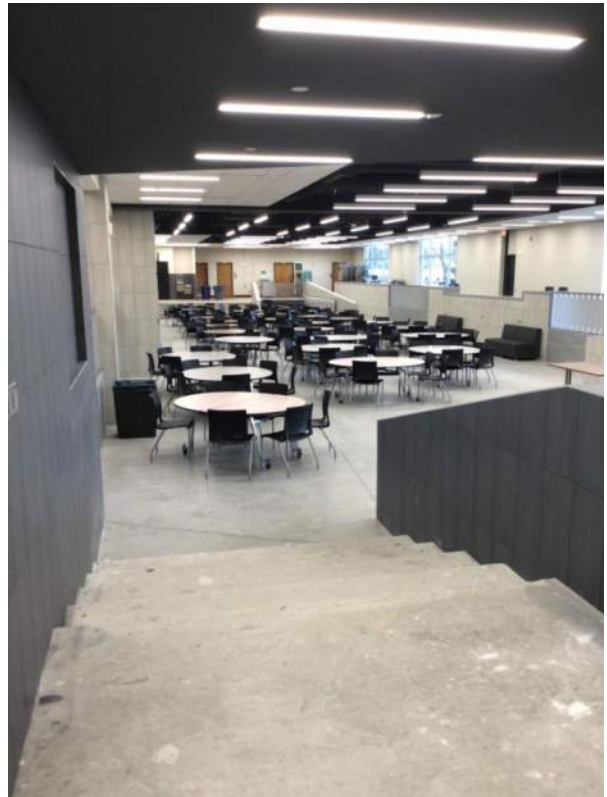**High School – Commons – acoustical wall panels and wall tile.**



	<p align="center"><b>ICS Weekly Project Report</b> December 13, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, December 10, 2021**
  - Continued punch list and commissioning items
  - Installed additional lockers
- **Planned for Week ending Friday, December 17, 2021**
  - Continue punch list and commissioning items

### **Middle School/High School Interior Renovations**

- **Completed Week/ ending Friday, December 10, 2021**
  - Middle School
    - Media Center – Completed wall tile.
    - Media Center – Completed new casework installation.
    - Restrooms – Started floor tile.
    - Completed student locker installation in the corridors and Special Ed. Toilet/Shower room.
    - Continued addressing punch list and commissioning items.
  - High School
    - Completed locker installation in the Special Ed. Toilet/Shower rooms.
    - Continued addressing punchlist and commissioning items.
- **Planned for Week ending Friday, December 17, 2021**
  - Middle School
    - Restrooms – Begin wall tile.
    - Continue addressing punch list and commissioning items.
  - High School
    - Continue addressing punch list and commissioning items.

### **Middle/High School Parking Lot**

- **Planned for Week ending Friday, December 10, 2021**
  - Continued to work on bid documents.
- **Planned for Week ending Friday, December 17, 2021**
  - Continue to work on bid documents.



ICS Weekly Project Report  
December 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley-Installed Additional Lockers







ICS Weekly Project Report  
December 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Media Center - wall tile.**





**ICS Weekly Project Report**  
December 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Student lockers – Sloped tops, closure panels and vinyl base installed.**





ICS Weekly Project Report  
December 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Student lockers – Sloped tops, closure panels and vinyl base installed.**








ICS Weekly Project Report  
December 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

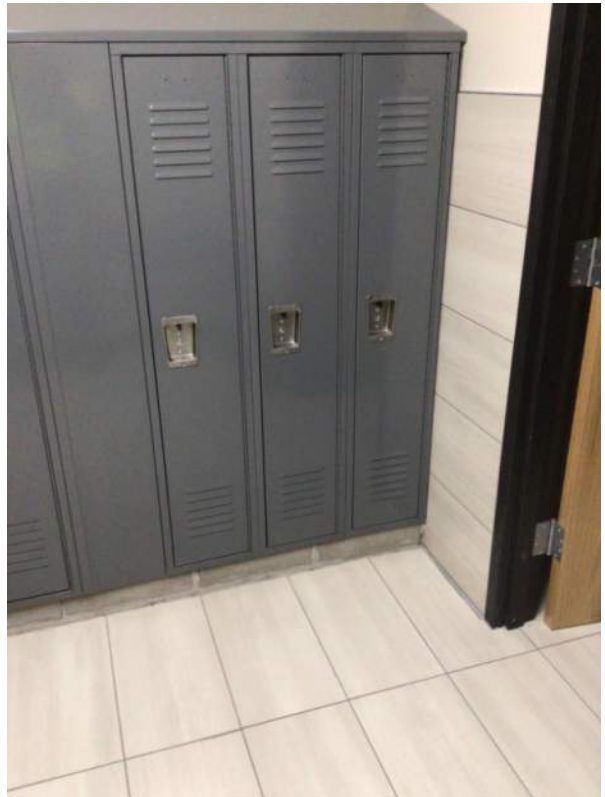**High School – Lockers – Special Ed. Toilet/Shower Rooms.**



	<p align="center"><b>ICS Weekly Project Report</b> December 20, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, December 17, 2021**
  - Continued punch list and commissioning items
- **Planned for Week ending Friday, December 24, 2021**
  - Continue punch list and commissioning items

**Middle School/High School Interior Renovations**

- **Completed Week/ ending Friday, December 17, 2021**
  - Middle School
    - Media Center – continued new casework installation.
    - Restrooms – completed floor tile and plumbing wall tile.
    - Continued addressing punch list and commissioning items.
  - High School
    - Resumed fire alarm device installation.
    - Continued addressing punch list and commissioning items.
- **Planned for Week ending Friday, December 24, 2021**
  - Middle School
    - Media Center – grout wall tile.
    - Media Center – complete plastic laminate panels and countertops.
    - Restrooms – continue wall tile.
    - Continue addressing punch list and commissioning items.
  - High School
    - Commons – begin ceiling acoustical baffle system.
    - Continue fire alarm device installation.
    - Continue addressing punch list and commissioning items.

**Middle/High School Parking Lot**

- **Planned for Week ending Friday, December 17, 2021**
  - Continued to work on bid documents.
- **Planned for Week ending Friday, December 24, 2021**
  - 75% progress construction bid documents to be issued




**ICS Weekly Project Report**  
December 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Restroom – plumbing wall tile work and wall prep.**

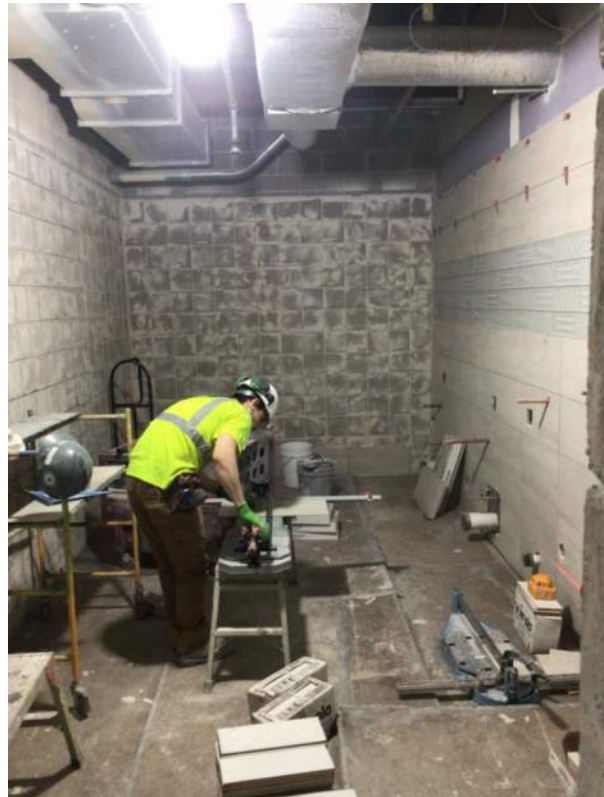





**ICS Weekly Project Report**  
December 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Media Center – Casework.**



	<p align="center"><b>ICS Weekly Project Report</b> December 27, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>



### **Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, December 24, 2021**
  - Continued punch list and commissioning items
  - Install wall and rough ins for cabinet unit heater in breezeway
- **Planned for Week ending Friday, December 31, 2021**
  - Continue punch list and commissioning items
  - Finish cabinet unit heater and wall installation in breezeway

### **Middle School/High School Interior Renovations**

- **Completed Week/ ending Friday, December 24, 2021**
  - Middle School
    - Media Center – started p-lam finish at the circulation and IT Help Desk.
    - Restrooms – continued setting wall tile.
    - Continued addressing punch list and commissioning items.
  - High School
    - Started acoustical baffle installation.
    - Continued addressing punch list and commissioning items.
- **Planned for Week ending Friday, December 31, 2021**
  - Middle School
    - Media Center – complete plastic laminate panels and countertops.
    - Restrooms – complete wall tile.
    - Restrooms – complete acoustical ceiling grid.
    - Continue addressing punch list and commissioning items.
  - High School
    - Commons – continue acoustical baffle installation.
    - Commons - stage delivery and supervised assembly/installation.
    - Commons - A/V installation.
    - Continue addressing punch list and commissioning items.



	<p><b>ICS Weekly Project Report</b> December 27, 2021</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Middle/High School Parking Lot**

- **Planned for Week ending Friday, December 24, 2021**
  - Continued to work on bid documents.
- **Planned for Week ending Friday, December 31, 2021**
  - Continue to work on bid documents.



ICS Weekly Project Report  
December 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley-Cabinet Unit Heater Rough In and Wall Installation





**ICS Weekly Project Report**  
December 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Restroom – wall tile installation**





ICS Weekly Project Report  
December 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Media Center – Circulation Desk p-lam finish.**

