


	<p align="center">ICS Weekly Project Report January 3, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, December 31, 2021**
 - Continued punch list and commissioning items
 - Finished cabinet unit heater and wall installation in breezeway
- **Planned for Week ending Friday, January 7, 2022**
 - Continue punch list and commissioning items

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, December 31, 2021**
 - Middle School
 - Media Center – completed p-lam finish at the Circulation and IT Help Desk.
 - Restrooms – completed tile, ceilings, lights, plumbing fixtures, partitions, accessories, and final inspections.
 - Restrooms – started demolition on the second set of restrooms to be renovated.
 - Athletic lockers were delivered to site and the installation is on-going.
 - Continued addressing punch list and commissioning items.
 - High School
 - Completed acoustical baffle installation.
 - Completed Commons A/V installation.
 - Miscellaneous terrazzo patching.
 - Continued addressing punch list and commissioning items.
 - Ordered scoreboards
- **Planned for Week ending Friday, January 7, 2022**
 - Middle School
 - Restrooms – complete demolition and begin plumbing rough-in.
 - Complete athletic lockers.
 - Continue addressing punch list and commissioning items.
 - High School
 - Continue addressing punch list and commissioning items.

	ICS Weekly Project Report January 3, 2022
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle/High School Parking Lot

- **Planned for Week ending Friday, December 31, 2021**
 - Continued to work on bid documents.
- **Planned for Week ending Friday, January 7, 2022**
 - Continue to work on bid documents.



ICS Weekly Project Report
January 3, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley-Cabinet Unit Heater and Wall Installation





ICS Weekly Project Report
January 3, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restroom – Ceilings, lights, plumbing fixtures, partitions, and accessories.





ICS Weekly Project Report

January 3, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Circulation Desk and IT Help Desk p-lam finishes.





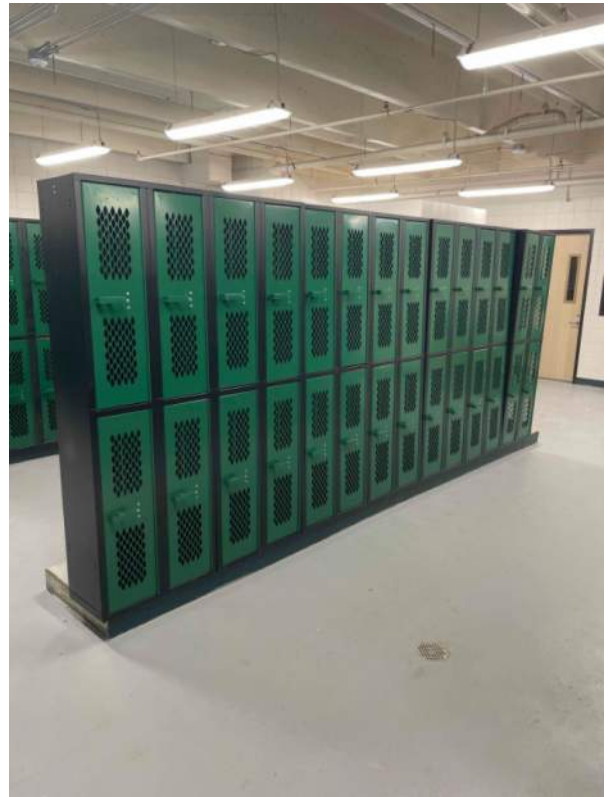
ICS Weekly Project Report

January 3, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Locker Rooms – Athletic lockers.





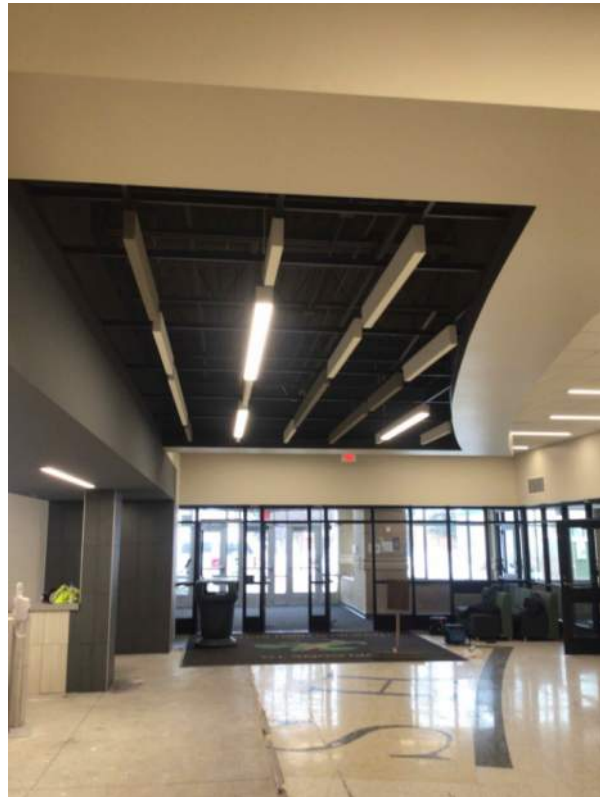
ICS Weekly Project Report



January 3, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons – Acoustical baffles.



	<p align="center">ICS Weekly Project Report January 10, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, January 7, 2022**
 - Continued punch list and commissioning items
- **Planned for Week ending Friday, January 14, 2022**
 - Continue punch list and commissioning items

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, January 7, 2022**
 - Middle School
 - Media Center – Installed aluminum storefronts.
 - Restrooms – Completed demo. Started plumbing rough-in.
 - Completed athletic locker install.
 - Continued addressing punch list and commissioning items.
 - High School
 - Continued addressing punchlist and commissioning items.
- **Planned for Week ending Friday, January 14, 2022**
 - Middle School
 - Restrooms – continue plumbing rough-in.
 - Continue addressing punch list and commissioning items.
 - High School
 - Continue addressing punch list and commissioning items.

Middle/High School Parking Lot

- **Planned for Week ending Friday, January 7, 2022**
 - Continued to work on bid documents.
- **Planned for Week ending Friday, January 14, 2022**
 - Continue to work on bid documents.



ICS Weekly Project Report
January 10, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Aluminum storefronts and wood doors.



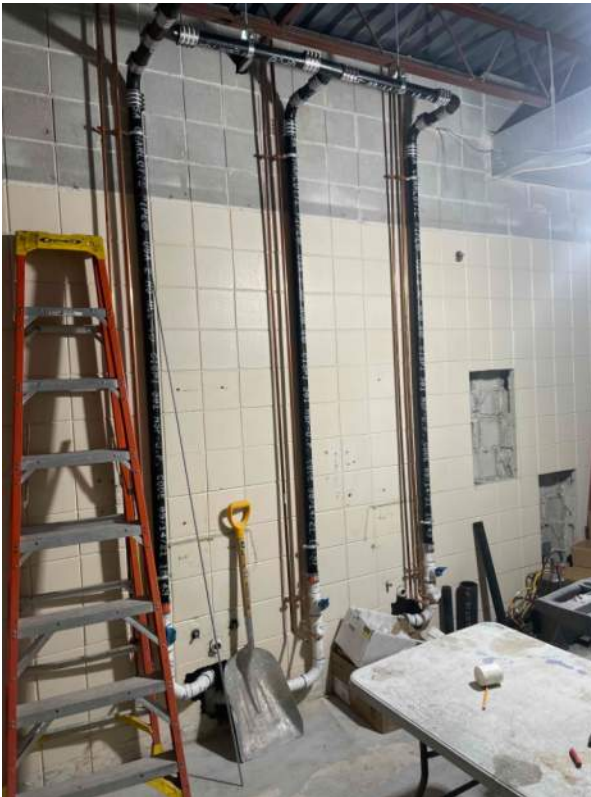




ICS Weekly Project Report
January 10, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restrooms – Plumbing rough-in.



	<p align="center">ICS Weekly Project Report January 17, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, January 14, 2022**
 - Continued punch list and commissioning items
- **Planned for Week ending Friday, January 21, 2022**
 - Continue punch list and commissioning items

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, January 14, 2022**
 - Middle School
 - Restrooms – Continued plumbing rough-in.
 - Continued addressing punch list and commissioning items.
 - High School
 - Continued addressing punch list and commissioning items.
- **Planned for Week ending Friday, January 21, 2022**
 - Middle School
 - Restrooms – Complete plumbing rough-in.
 - Restrooms – Begin wall framing and drywall.
 - Continue addressing punch list and commissioning items.
 - High School
 - Continue addressing punch list and commissioning items.

Middle/High School Parking Lot

- **Planned for Week ending Friday, January 14, 2022**
 - Continued to work on bid documents.
- **Planned for Week ending Friday, January 21, 2022**
 - Continue to work on bid documents.
 - Work on presentation to POC and School Board





ICS Weekly Project Report
January 17, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restrooms – Plumbing rough-in.



	<p align="center">ICS Weekly Project Report January 24, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, January 21, 2022**
 - Continued punch list and commissioning items
- **Planned for Week ending Friday, January 28, 2022**
 - Continue punch list and commissioning items

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, January 21, 2022**
 - Middle School
 - Restrooms – Completed plumbing rough-in and inspections.
 - Restrooms – Started metal stud framing.
 - Continued addressing punch list and commissioning items.
 - High School
 - Continued addressing punch list and commissioning items.
- **Planned for Week ending Friday, January 28, 2022**
 - Middle School
 - Restrooms – Complete drywall.
 - Continue addressing punch list and commissioning items.
 - High School
 - Continue addressing punch list and commissioning items.

Middle/High School Parking Lot

- **Planned for Week ending Friday, January 21, 2022**
 - Continued to work on bid documents.
- **Planned for Week ending Friday, January 28, 2022**
 - Finished bid documents.
 - ICS to present to School Board to get approval to send out bid documents to contractors
 - Issue bid documents



ICS Weekly Project Report
January 24, 2022



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restrooms – Plumbing rough-in and metal stud framing.

