


	<p align="center">ICS Weekly Project Report November 1, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, October 29, 2021**
 - Continued commissioning of mechanical system
 - Delivered and installed administration new furniture
- **Planned for Week ending Friday, November 5, 2021**
 - Continue commissioning of mechanical system
 - Delivered wall covering and staged for installation

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, October 29, 2021**
 - Middle School
 - Continued installing backordered permanent doors and hardware.
 - Continued installing backordered markerboards and tackboards.
 - Media Center – continued drywall tape, mud and sand.
 - Media Center – completed in-wall plumbing rough-in.
 - Phase 2 Restrooms – completed plumbing wall framing and started in-wall plumbing rough-in.
 - Furniture installers continued assembling and placing backordered furniture pieces.
 - High School
 - Continued installing backordered permanent doors and hardware.
 - Continued installing backordered markerboards and tackboards.
 - Continued Commons wall tile.
 - Furniture installers to continue assembling and placing backordered furniture pieces.
- **Planned for Week ending Friday, November 5, 2021**
 - Middle School
 - Media Center – begin painting walls.
 - Media Center – complete concrete in-fills at underground rough-in locations.
 - Phase 2 Restrooms – pour back concrete slabs.
 - Phase 2 Restrooms – in-wall rough-in inspections.
 - High School

	ICS Weekly Project Report November 1, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

- Complete p-lam benches in the Commons.
- Continue tile work in the Commons.
- Contractors to continue addressing punchlist items and misc. touch-ups.

Stadium Light Replacement .

- **Completed for Week ending Friday, October 29, 2021**
 - ICS reviewed costs and designs to POC
- **Planned for Week ending Friday, November 5, 2021**
 - ICS to meet with Activities Director, coaches, and Facilities Director and review design, costs, and schedule



ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley –Administration Furniture Delivery and Installation






ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Administration Furniture Delivery and Installation





ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – drywall taping and sanding.






ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Phase 2 Restrooms – in-wall plumbing rough-in .

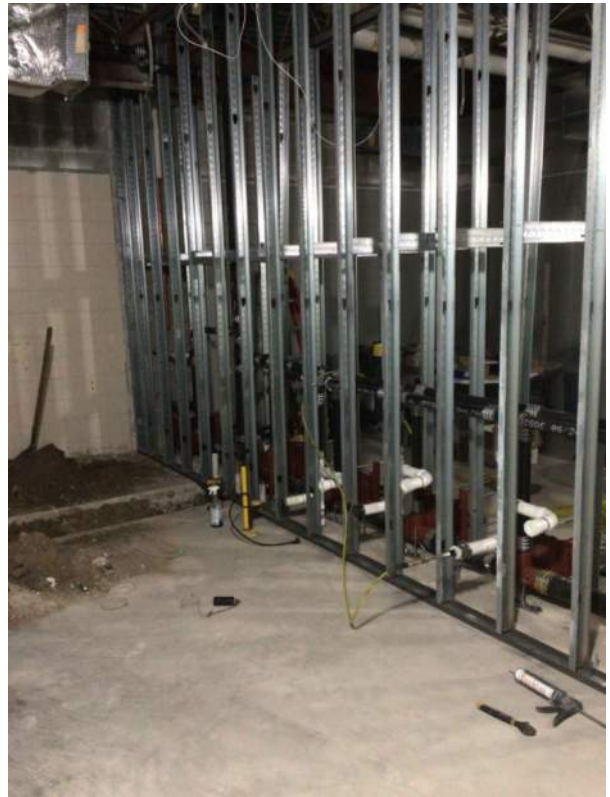



ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Furniture delivery and installation.





ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons tile work.






ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Furniture delivery and installation.

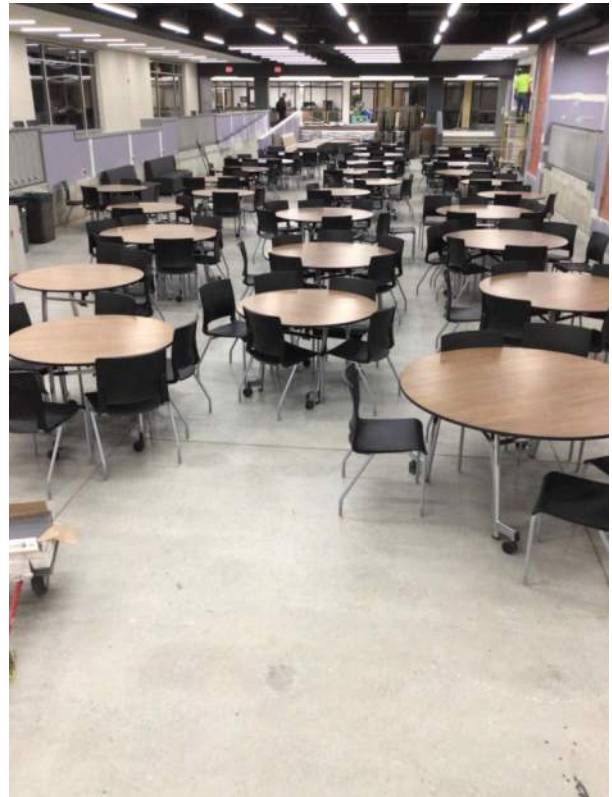





ICS Weekly Project Report
November 1, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Furniture delivery and installation.



	<p align="center">ICS Weekly Project Report November 8, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>



Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, November 5, 2021**
 - Continued commissioning of mechanical system
 - Delivered wall covering and staged for installation
- **Planned for Week ending Friday, November 12, 2021**
 - Install wall covering
 - Summer phase furniture user group meetings

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, November 5, 2021**
 - Middle School
 - Media Center – Complete circulation desk and IT Help Desk framing and sheathing.
 - Media Center – Started painting soffits and walls.
 - Media Center – Completed overhead mechanical and electrical rough-in.
 - Restrooms – Completed waste and vent piping. Started domestic water piping.
 - High School
 - Commons – Continued wall tile and completed grouting about 75% of the tile installed.
- **Planned for Week ending Friday, November 12, 2021**
 - Middle School
 - Media Center – Continue painting walls and soffits.
 - Media Center – Start acoustical ceiling grid and mechanical and electrical ceiling finishes.
 - Restrooms – Complete domestic water piping and begin wall sheathing.
 - Condensing unit coil replacements.
 - Continue addressing punchlist items and misc. touch-ups.
 - High School
 - Commons – Continue wall tile installation.
 - Continue addressing punchlist items and misc. touch-ups.

Stadium Light Replacement .

	ICS Weekly Project Report November 8, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

- **Completed for Week ending Friday, November 5, 2021**
 - ICS met with Activities Director, and Facilities Director to review design, costs, and schedule
- **Planned for Week ending Friday, November 12, 2021**
 - Issue Purchase Order

Middle/High School Parking Lot

- **Planned for Week ending Friday, November 12, 2021**
 - Complete initial cost estimate



ICS Weekly Project Report
November 8, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Media circulation desk and IT Help Desk.





ICS Weekly Project Report
November 8, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Break-Out Room and Dist. IT Storage.





ICS Weekly Project Report
November 8, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restroom Progress.









ICS Weekly Project Report
November 8, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

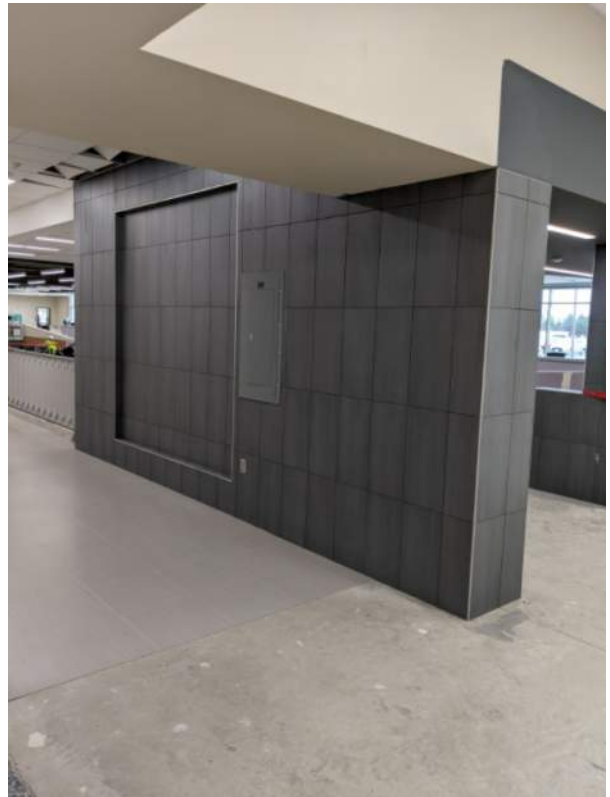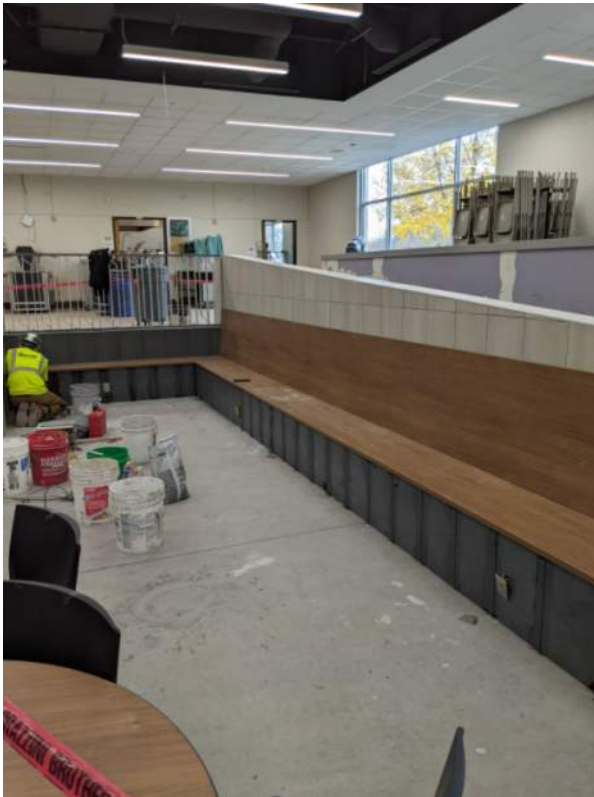High School – Commons tile work.





	<p align="center">ICS Weekly Project Report November 15, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, November 12, 2021**
 - Installed wall covering
 - Furniture user group meeting took place for next phase
- **Planned for Week ending Friday, November 19, 2021**
 - Continue punch list and commissioning items
 - Send out specifications for furniture to vendors for proposals

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, November 12, 2021**
 - Middle School
 - Media Center – Continued painting walls, soffits, and hollow metal door frames.
 - Media Center – Started acoustical ceiling.
 - Media Center – Started installing light fixtures, PA system speakers, and mechanical diffusers in the ceiling space.
 - Restrooms – Completed domestic water piping and piping insulation.
 - Continued addressing punch list items and misc. touch-ups.
 - High School
 - Commons – Continue wall tile installation.
 - Continued addressing punch list items and misc. touch-ups.
- **Planned for Week ending Friday, November 19, 2021**
 - Middle School
 - Media Center – Complete mechanical and electrical ceiling finishes.
 - Media Center – Start installing acoustical ceiling tiles.
 - Media Center – Begin installing flooring, LVT and carpet tiles.
 - Restrooms – Begin installing wall sheathing at plumbing walls.
 - Continue addressing punch list items and misc. touch-ups.
 - High School
 - Commons – Continue wall tile installation.
 - Continue addressing punch list items and misc. touch-ups.

	<p>ICS Weekly Project Report November 15, 2021</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

Stadium Light Replacement

- **Completed for Week ending Friday, November 12, 2021**
 - Issued purchase order to Musco Lighting

Middle/High School Parking Lot

- **Planned for Week ending Friday, November 19, 2021**
 - Cost estimates for scope of work




ICS Weekly Project Report
November 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley-Wall Covering Installed

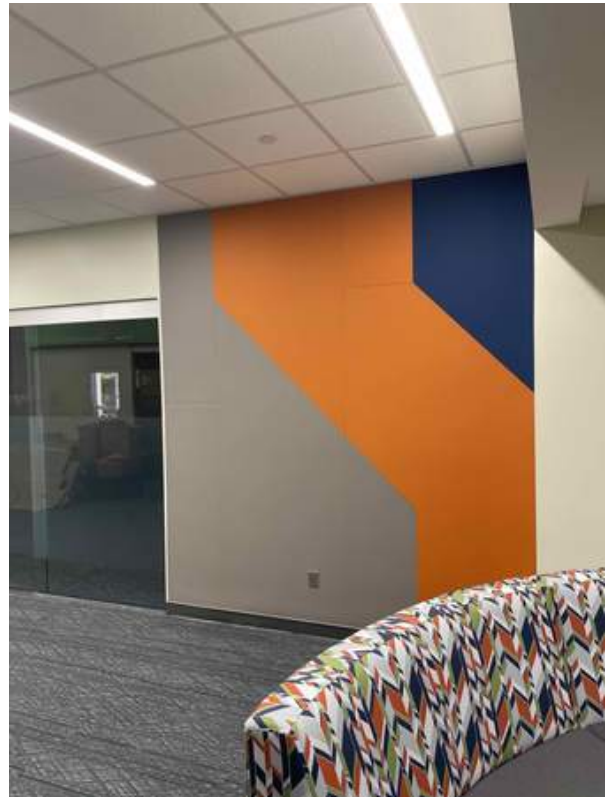




ICS Weekly Project Report
November 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Painting on-going. Ceiling grid and mechanical and electrical ceiling finishes completed.

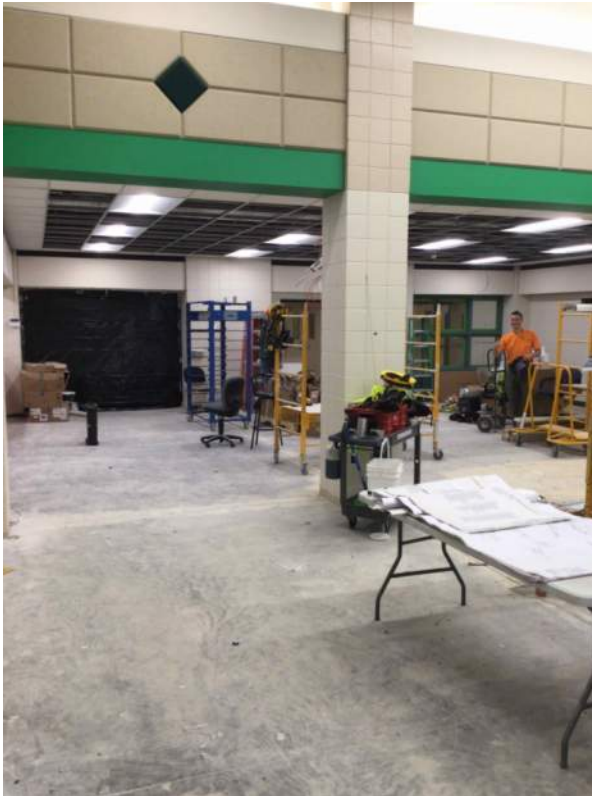



ICS Weekly Project Report
November 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restrooms – Plumbing piping and insulation completed.





ICS Weekly Project Report
November 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons tile on-going.








ICS Weekly Project Report
November 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

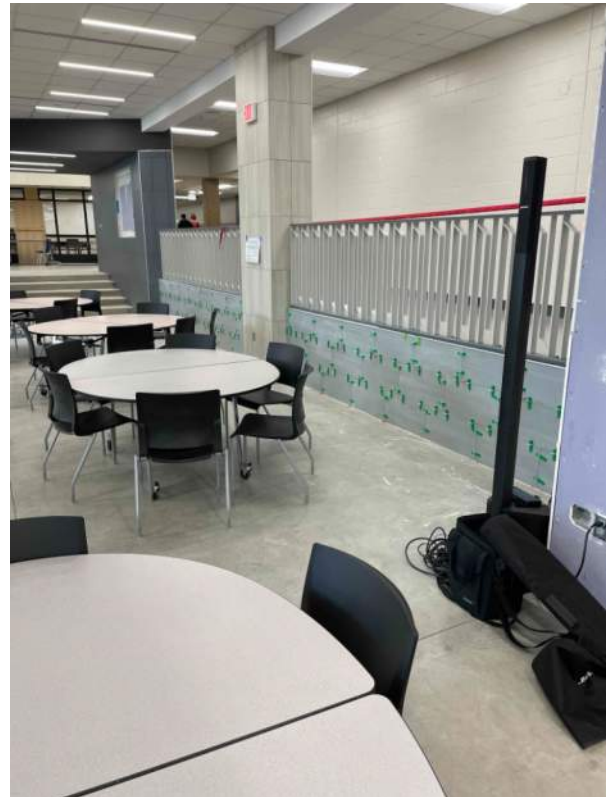High School – Commons tile on-going.





	<p align="center">ICS Weekly Project Report November 22, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, November 19, 2021**
 - Continued punch list and commissioning items
 - Sent out specifications for furniture to vendors for proposals
- **Planned for Week ending Friday, November 26, 2021**
 - Continue punch list and commissioning items

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, November 19, 2021**
 - Middle School
 - Media Center – Continued painting walls, soffits and hollow metal frames.
 - Media Center – Started installing acoustical ceiling tiles.
 - Media Center – Started installing carpet tiles and LVT.
 - Media Center – Started installing markerboards.
 - Restrooms – Completed tile backer board installation on the plumbing walls.
 - Continued addressing punch list items and misc. touch-ups.
 - High School
 - Commons/Lobby – Continued wall tile installation.
 - Installed interior secure vestibule aluminum framing.
 - Continued addressing punch list items and misc. touch-ups.
- **Planned for Week ending Friday, November 26, 2021**
 - Middle School
 - Media Center – Continue installing carpet tiles and LVT.
 - Media Center – Complete mechanical ceiling finishes and install remaining acoustical ceiling tiles.
 - Restrooms – Tile work surface prep.
 - Continue addressing punch list items and misc. touch-ups.
 - High School
 - Commons – Complete all remaining wall tile.
 - Commons – Complete acoustical wall panels.
 - Continue addressing punch list items and misc. touch-ups.

	<p>ICS Weekly Project Report November 22, 2021</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle/High School Parking Lot

- **Planned for Week ending Friday, November 19, 2021**
 - Completed cost estimate
- **Planned for Week ending Friday, November 26, 2021**
 - Continue to work on bid documents



ICS Weekly Project Report
November 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Wall and floor finishes.






ICS Weekly Project Report
November 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center – Wall and floor finishes.

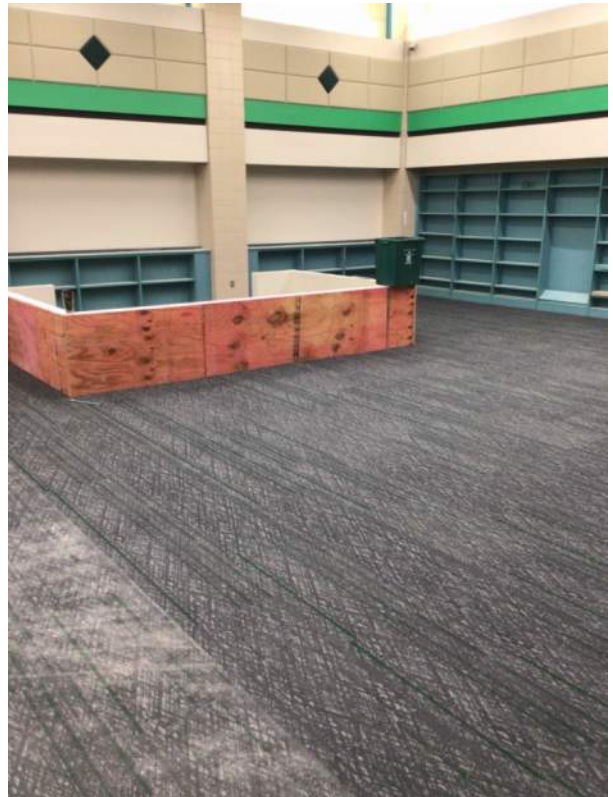



ICS Weekly Project Report
November 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restrooms – Tile backer board installed on plumbing walls.





ICS Weekly Project Report
November 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Lobby and Servery wall tile.







ICS Weekly Project Report
November 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons wall tile.

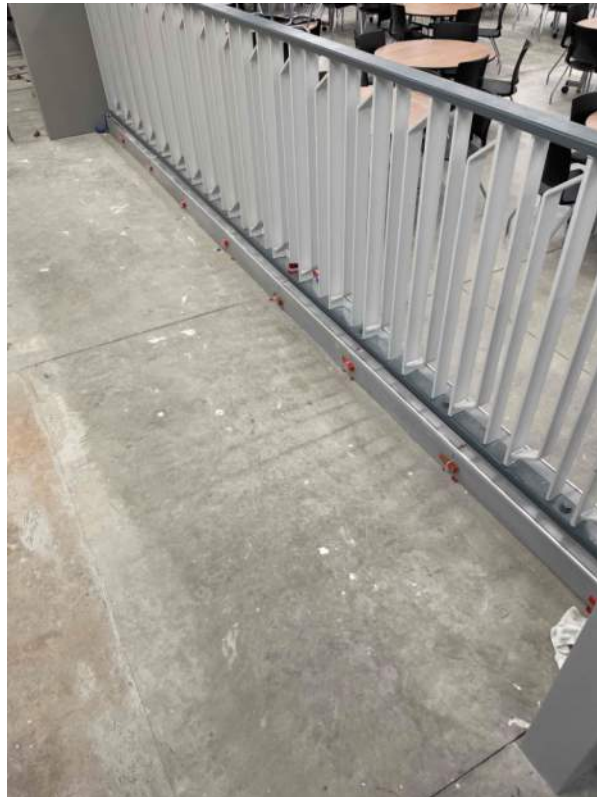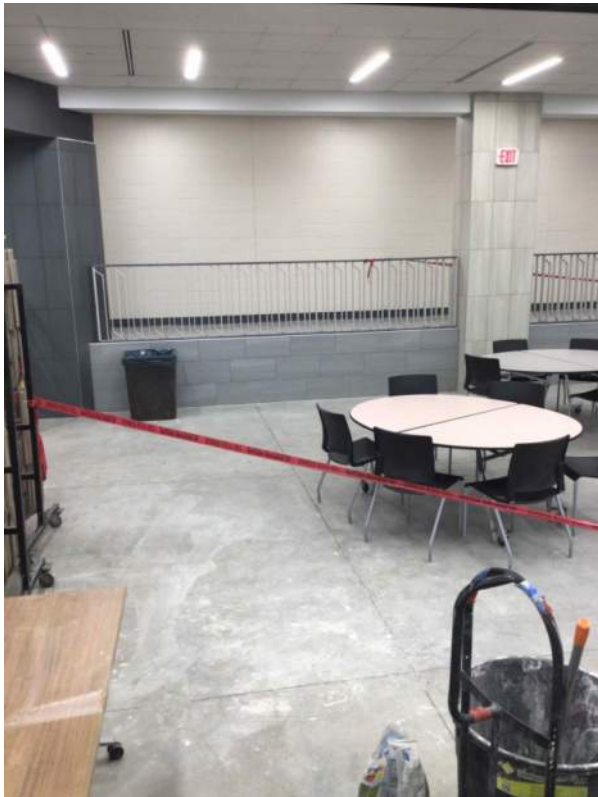





ICS Weekly Project Report
November 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Secure vestibule aluminum framing.





	<p align="center">ICS Weekly Project Report November 29, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, November 26, 2021**
 - Continued punch list and commissioning items
- **Planned for Week ending Friday, December 3, 2021**
 - Continue punch list and commissioning items

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, November 26, 2021**
 - Middle School
 - Media Center – Completed painting.
 - Media Center – Completed all mechanical and electrical ceiling finishes.
 - Media Center – Continued installing flooring and wall base.
 - Started student locker installation in the corridors.
 - Continued addressing punch list and commissioning items.
 - High School
 - Commons – Wall tile nearing completion.
 - Installed glass in the aluminum storefront vestibule framing.
 - Continued addressing punch list and commissioning items.
- **Planned for Week ending Friday, December 3, 2021**
 - Middle School
 - Media Center – Above ceiling inspections scheduled
 - Media Center – Complete acoustical ceiling tiles.
 - Media Center – Begin wall tile.
 - Continue student locker installation in the corridors.
 - Continue addressing punch list and commissioning items.
 - High School
 - Commons – Complete all remaining wall tile and begin grouting tile joints.
 - Commons – Complete acoustical wall panels.
 - Continue addressing punch list and commissioning items.

	<p>ICS Weekly Project Report November 29, 2021</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

Middle/High School Parking Lot

- **Planned for Week ending Friday, November 26, 2021**
 - Continued to work on bid documents.
- **Planned for Week ending Friday, December 3, 2021**
 - Continue to work on bid documents.




ICS Weekly Project Report
November 29, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Student lockers.

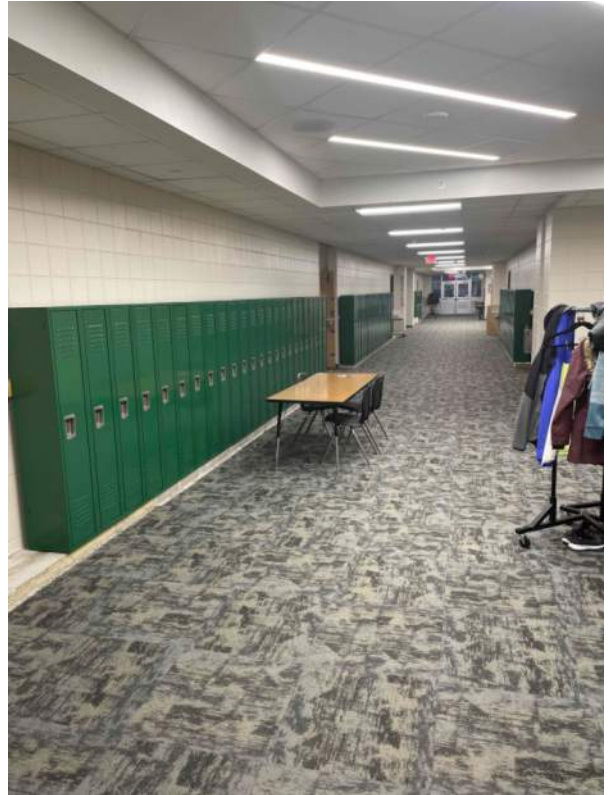



ICS Weekly Project Report
November 29, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons – tile work.

