
	<p align="center"><b>ICS Weekly Project Report</b> May 2, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, April 29, 2022**
  - Continued boiler room new piping
  - Delivery of some of the new boiler room equipment, pumps, boilers, tanks
- **Planned for Week ending Friday, May 6, 2022**
  - Continue new piping in boiler room
  - Set/stage equipment in boiler room

### **Middle School/High School Interior Renovations**

- **Completed Week ending Friday, April 29, 2022**
  - Middle School – Restrooms – Began floor and wall prep for tile installation.
- **Planned for Week ending Friday, May 6, 2022**
  - Middle School – Restrooms – Complete floor and wall prep for tile installation.
  - Middle School – Restrooms – Begin tile installation.

### **Middle/High School Parking Lot**

- **Completed for Week ending Friday, April 29, 2022**
  - Continued submittals and material procurement
  - Construction coordination meeting took place 04/26
- **Planned for Week ending Friday, May 6, 2022**
  - Continue submittals and material procurement

### **Stadium Lights**

- **Completed for Week ending Friday, April 29, 2022**
  - Backfilled trenches
- **Planned for Week ending Friday, May 6, 2022**
  - Wait for opening of asphalt plants for asphalt paving



ICS Weekly Project Report  
May 2, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley – Boiler Room and Some Equipment Delivery







ICS Weekly Project Report  
May 2, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Stadium Lights - Backfill Electrical Trenches and Old Light Bases**



	<p align="center"><b>ICS Weekly Project Report</b> May 9, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, May 6, 2022**
  - Boiler Room new piping and setting of new equipment
- **Planned for Week ending Friday, May 13, 2022**
  - Shut down and remove small boiler and components

**Middle School/High School Interior Renovations**

- **Completed Week ending Friday, May 6, 2022**
  - Middle School – Restrooms – Completed wall and floor prep for tile installation.
  - Middle School – Restrooms – Started tile installation.
  - High School – Phase 3 – Continued preconstruction coordination.
- **Planned for Week ending Friday, May 13, 2022**
  - Middle School – Restrooms – Complete tile installation.

**Middle/High School Parking Lot**

- **Completed for Week ending Friday, May 6, 2022**
  - Put together overall schedule
  - Shop drawings and submittal review and approval
- **Planned for Week ending Friday, May 13, 2022**
  - Continue shop drawing and submittal review



ICS Weekly Project Report  
May 9, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley – Boiler Room New Piping and Equipment







**ICS Weekly Project Report**  
May 9, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Restrooms – Tile installation**



	<p align="center"><b>ICS Weekly Project Report</b> May 16, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, May 13, 2022**
  - Shut down and removed small boiler and components
  - Boiler Room new piping and setting of new equipment
- **Planned for Week ending Friday, May 20, 2022**
  - Boiler Room new piping

**Middle School/High School Interior Renovations**

- **Completed Week ending Friday, May 13, 2022**
  - Middle School – Restrooms – Completed tile installation.
  - Middle School – Restrooms – Continued overhead plumbing, mechanical and electrical.
  - High School – Phase 3 – Continued preconstruction planning.
- **Planned for Week ending Friday, May 20, 2022**
  - Middle School – Restrooms – Set plumbing fixtures.
  - High School – Phase 3 – Continue preconstruction planning.

**Middle/High School Parking Lot**

- **Completed for Week ending Friday, May 13, 2022**
  - Continued shop drawing and submittal review
- **Planned for Week ending Friday, May 20, 2022**
  - Continue shop drawing and submittal review




ICS Weekly Project Report  
May 16, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley – Boiler Room New Piping

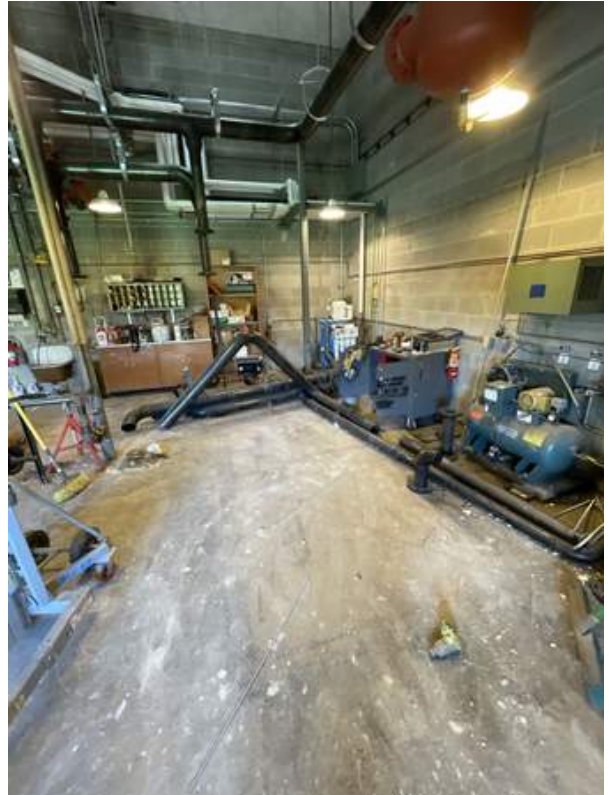







ICS Weekly Project Report  
May 16, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Restrooms – Tile work completed.**



	<p align="center"><b>ICS Weekly Project Report</b> May 23, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, May 20, 2022**
  - Formed and poured concrete pads for mechanical equipment
- **Planned for Week ending Friday, May 27, 2022**
  - Set mechanical equipment on concrete pads

**Middle School/High School Interior Renovations**

- **Completed Week ending Friday, May 20, 2022**
  - Middle School – Restrooms – Completed plumbing fixture installation.
  - High School – Phase 3 – Continued preconstruction planning.
- **Planned for Week ending Friday, May 27, 2022**
  - Middle School – Restrooms – Complete acoustical ceiling grid.
  - Middle School – Restrooms – Install lights, grilles and diffusers.
  - High School – Phase 3 – Continue preconstruction planning.

**Middle/High School Parking Lot**

- **Completed for Week ending Friday, May 20, 2022**
  - Shop drawing review, ordering of materials
- **Planned for Week ending Friday, May 27, 2022**
  - Construction coordination meeting scheduled 5/24





**ICS Weekly Project Report**  
May 23, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley – Boiler Room Formed and Poured Concrete Pads**

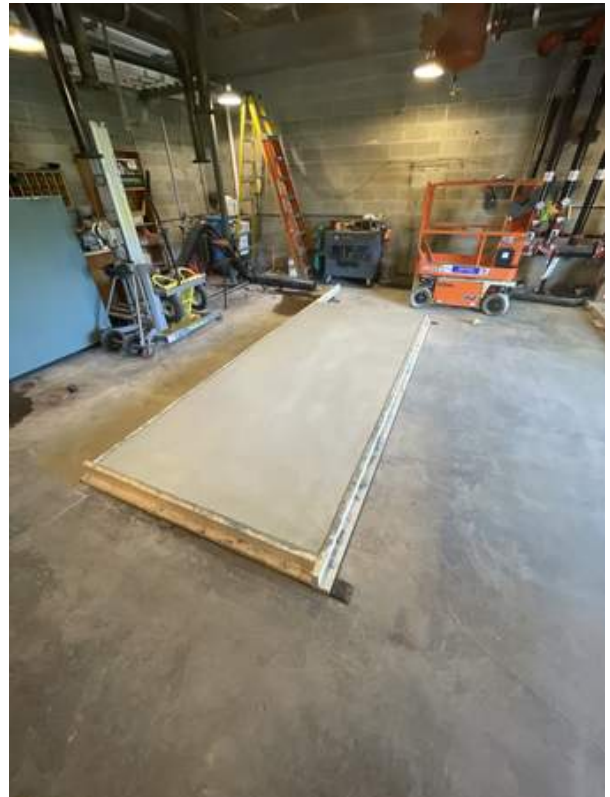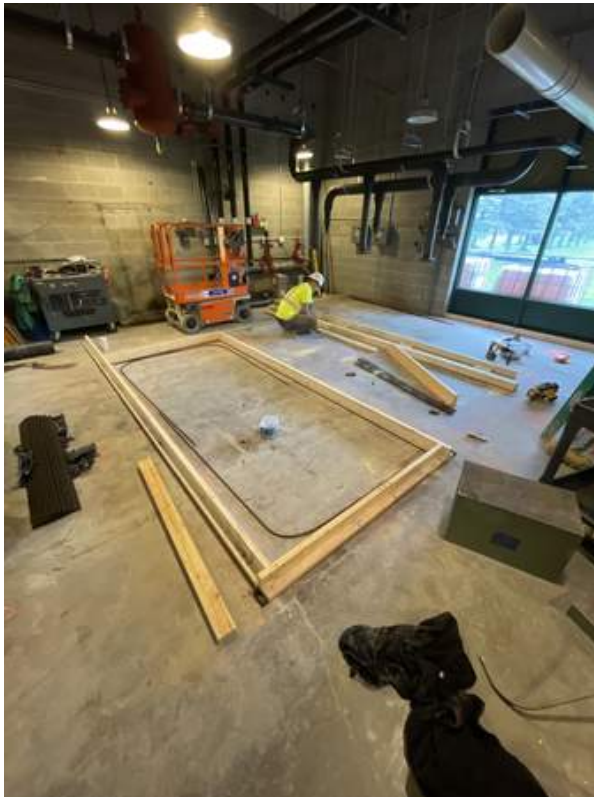





**ICS Weekly Project Report**  
May 23, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Restrooms – Plumbing fixtures installed.**





	<p align="center"><b>ICS Weekly Project Report</b> May 31, 2022</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Lake Ripley Elementary Interior Renovations**

- **Completed Week ending Friday, May 27, 2022**
  - Boiler Room
    - Set mechanical equipment on concrete pads
    - Hang ductwork
- **Planned for Week ending Friday, June 3, 2022**
  - Boiler Room
    - Hang ductwork
    - Shut down domestic water for temporary hook ups
  - Hallways/Classrooms
    - Place floor protection and temporary walls
    - Staff move out-remove furniture, and technology
  - Bathrooms
    - Abatement and demolition
  - Roof work
    - Material delivery

### **Middle School/High School Interior Renovations**

- **Completed Week ending Friday, May 27, 2022**
  - Middle School – Restrooms – Completed acoustical ceiling grid.
  - Middle School – Restrooms – Began installing mechanical and electrical ceiling finishes.
  - High School – CTE – Completed greenhouse demolition.
  - High School – Contractors began pre-fabricating piping and assembling duct work on-site.
- **Planned for Week ending Friday, June 3, 2022**
  - Middle School – Restrooms – Complete mechanical and electrical ceiling finishes.
  - Middle School – Restrooms – Complete acoustical ceiling tile installation.
  - Middle School – Restrooms – Complete toilet partitions.
  - High School – Complete Owner move-out and removal efforts.
  - Complete remaining scoreboard installations.
  - Resume punchlist item completion and verification.

	<p><b>ICS Weekly Project Report</b> May 31, 2022</p>
	<p>ISD #465 Litchfield Public Schools 2019 Referendum</p>

**Middle/High School Parking Lot**

- **Completed for Week ending Friday, May 27, 2022**
  - Construction coordination meeting held 5/24
- **Planned for Week ending Friday, June 3, 2022**
  - Preparation to mobilize



ICS Weekly Project Report  
May 31, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley – Boiler Room Progress-Boilers Set-Ductwork Installation**






ICS Weekly Project Report  
May 31, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Restrooms – Acoustical ceiling grid, mechanical ceiling finishes and toilet partitions.**

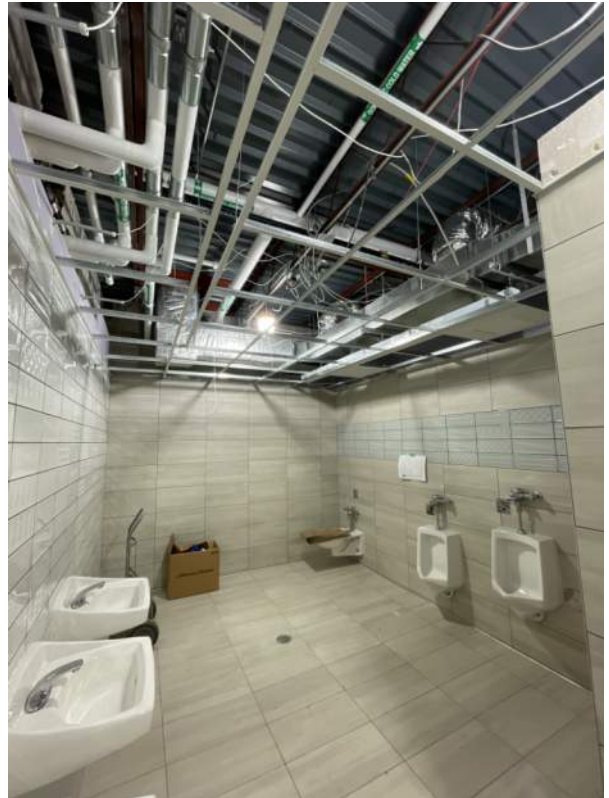





ICS Weekly Project Report  
May 31, 2022



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Greenhouse demolition and duct work assemblies.**

