
	<p align="center">ICS Weekly Project Report October 4, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>



Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, October 1, 2021**
 - Continued punch list
 - Camera terminations and programming
 - Continued programming and graphics on building automation system (BAS) interface
 - Turned over old cafeteria/new multipurpose room for occupancy

- **Planned for Week ending Friday, October 8, 2021**
 - Continue punch list
 - Commissioning of mechanical system
 - Troubleshoot paging system and speakers

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, October 1, 2021**
 - Middle School
 - Complete tile installation in the Boys Locker Rooms.
 - Completed plumbing fixtures in the Special Ed. Toilet/Shower room.
 - Started installing specialties in the Toilet/Shower room and Boys Locker Room.
 - Continued installing wall base and flooring transitions.
 - Started overhead mechanical and electrical rough-in in the Media Center.
 - Continued installing PA system cabling and speakers.
 - Continued installing camera cabling for Owner provided cameras.
 - High School
 - Continued painting handrails and soffits in the Commons.
 - Installed data rack in the Commons.
 - Continued installing wall base and flooring transitions.
 - Solid surface tops and plastic laminate benches in the Commons are nearing completion.
 - Tile work in the Toilet/Shower rooms and single occupancy Toilet rooms is nearing completion.
 - Continued installing PA system cabling and speakers.
 - Continued installing camera cabling for Owner provided cameras.

	<p align="center">ICS Weekly Project Report October 4, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- **Planned for Week ending Friday, October 8, 2021**
 - Middle School
 - Complete tile installation in the Girls Locker Rooms.
 - Continue installing plumbing fixtures in the Locker Rooms.
 - Continue installing specialties in the Toilet/Shower room and Locker Rooms.
 - Begin metal stud framing and in-wall rough-in in the Media Center.
 - High School
 - Complete tile work in the Toilet/Shower rooms and single occupancy Toilet rooms.
 - Continue plumbing fixtures and specialties in the Toilet/Shower rooms and single occupancy Toilet rooms.
 - Start tile work in the Commons.
 - Complete solid surface tops and plastic laminate benches in the Commons.

Stadium Light Replacement .

- **Completed for Week ending Friday, October 1, 2021**
 - Scheduled meeting with Musco Lighting to review scope and schedule.
- **Planned for Week ending Friday, October 8, 2021**
 - Meet with Musco Lighting to review scope and schedule.

Middle School/High School Parking Lot

- **Planned for Week ending Friday, October 8, 2021**
 - Reconvene design meetings with design team
 - Schedule user group meeting to review design



ICS Weekly Project Report
October 4, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center demo and rough-in progress.





ICS Weekly Project Report
October 4, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Boys Locker Room Tile and plumbing fixtures.





ICS Weekly Project Report
October 4, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Plumbing Fixtures in the SPED Toilet/Shower rooms.







ICS Weekly Project Report
October 4, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons progress showing p-lam benches installed.



	<p align="center">ICS Weekly Project Report October 11, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>



Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, October 8, 2021**
 - Continued punch list
 - Commissioning of mechanical system
 - Troubleshoot paging system and speakers
 - Installed back ordered drinking stations

- **Planned for Week ending Friday, October 15, 2021**
 - Commissioning of mechanical system
 - Delivery of back ordered display millwork
 - Continue graphics for the building automation system (BAS)

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, October 8, 2021**
 - Middle School
 - Completed plumbing fixtures and specialties installation in the Toilet/Shower room.
 - Completed Locker Room tile work.
 - Completed Locker Room plumbing fixtures. Specialties are on-going.
 - Started installing markerboards.
 - Media Center metal stud wall framing is complete. In-wall electrical rough-in is on-going.
 - PA system cabling and speakers installation is nearing completion.
 - Camera cabling for Owner provided cameras is nearing completion.
 - High School
 - Completed tile work in the Toilet/Shower rooms and single occupancy Toilet rooms.
 - Completed plumbing fixtures and specialties in the Toilet/Shower rooms and single occupancy Toilet rooms.
 - Started tile work in the Commons.
 - Continued installing PA system cabling and speakers.
 - Continued installing camera cabling for Owner provided cameras.

	<p align="center">ICS Weekly Project Report October 11, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Completed solid surface tops in the Commons.
- **Planned for Week ending Friday, October 15, 2021**
 - Middle School
 - Continue installing markerboards and tackboards.
 - Media Center – complete in-wall electrical rough-in and begin hanging drywall.
 - Complete specialties installation in the Locker Rooms.
 - Contractors to continue addressing punchlist items.
 - High School
 - Continue tile work in the Commons.
 - Continue misc. painting in the Commons.
 - Complete acoustical ceiling tiles in the Toilet rooms.
 - Start bench cushion installation in the Commons.
 - Start installing markerboards and tackboards.
 - Contractors to continue addressing punchlist items.
 - Continue installing PA system cabling and speakers.
 - Continu installing camera cabling for Owner provided cameras.

Stadium Light Replacement .

- **Completed for Week ending Friday, October 8, 2021**
 - Meeting held with Musco Lighting to review scope and schedule
- **Planned for Week ending Friday, October 15, 2021**
 - Musco working on design and proposal

Middle School/High School Parking Lot

- **Completed for Week ending Friday, October 8, 2021**
 - Reconvened design meetings with design team
 - Scheduled user group meeting to review design
- **Planned for Week ending Friday, October 15, 2021**
 - Meeting with Principals on current design



ICS Weekly Project Report
October 11, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Drinking Fountain Stations Installed





ICS Weekly Project Report
October 11, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center wall framing and in-wall rough-in.





ICS Weekly Project Report
October 11, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Locker Room partitions.






ICS Weekly Project Report
October 11, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Common soffit painting and wall tile.

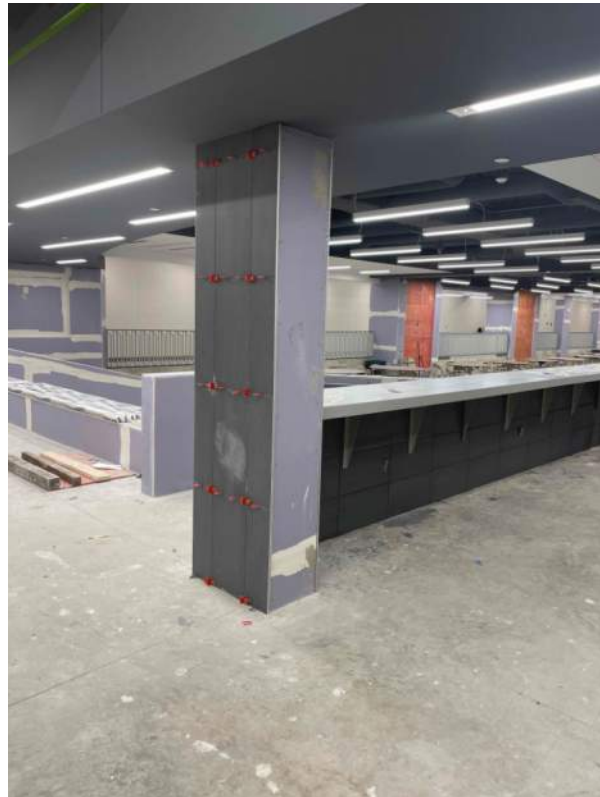





ICS Weekly Project Report
October 11, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Toilet/Shower room plumbing fixtures and specialties.





	<p align="center">ICS Weekly Project Report October 18, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, October 15, 2021**
 - Continued commissioning of mechanical system
 - Continued graphics for the building automation system (BAS)
- **Planned for Week ending Friday, October 22, 2021**
 - Continue commissioning of mechanical system
 - Training scheduled for the controls and building automation system (BAS)
 - Install back ordered paging speakers

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, October 15, 2021**
 - Middle School
 - Continued installing markerboards and tackboards.
 - Specialties installation in the Locker Rooms is nearing completion.
 - Contractors continued addressing punch list items.
 - Media Center – completed in-wall electrical rough-in and began hanging drywall.
 - High School
 - Continued tile work in the Commons.
 - Completed acoustical ceiling tiles in the Toilet rooms.
 - Started installing markerboards and tackboards.
 - Contractors continued addressing punch list items.
 - Continued installing PA system cabling and speakers.
- **Planned for Week ending Friday, October 22, 2021**
 - Middle School
 - Contractors to continue addressing punch list items.
 - Complete inspections and turn-over Toilet and Locker Rooms.
 - Media Center – continue hanging and finishing drywall.
 - High School
 - Contractors to continue addressing punch list items.
 - Complete inspections and turn-over Toilet Rooms.

	ICS Weekly Project Report October 18, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

- Complete reception desk p-lam finish.
- Complete Commons p-lam benches.
- Complete Commons acoustical wall panels and baffles.
- Continue Commons wall tile.

Stadium Light Replacement .

- **Completed for Week ending Friday, October 15, 2021**
 - Musco worked on design and proposal
- **Planned for Week ending Friday, October 22, 2021**
 - Musco to finish initial design and proposal



ICS Weekly Project Report
October 18, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center drywall on-going.





ICS Weekly Project Report
October 18, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Locker Room toilet and shower stall partitions.






ICS Weekly Project Report
October 18, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Corridor wall tile.

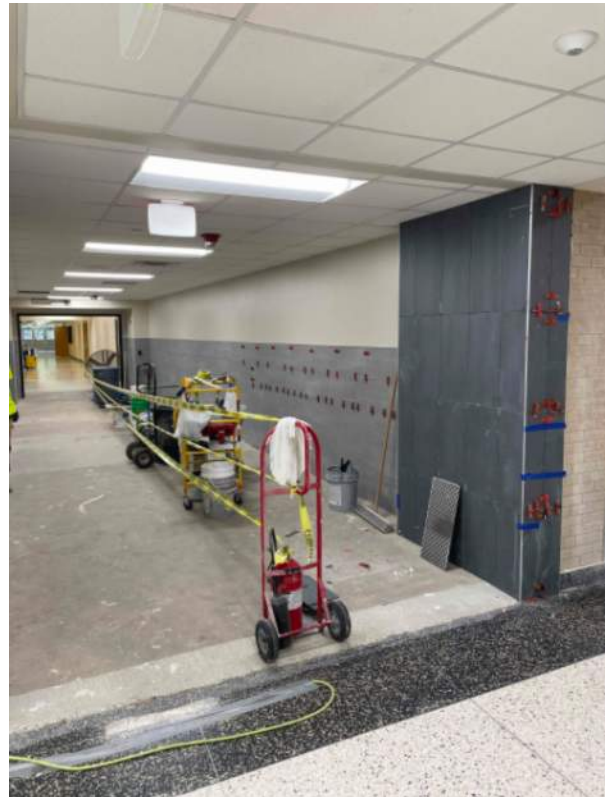






ICS Weekly Project Report
October 18, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

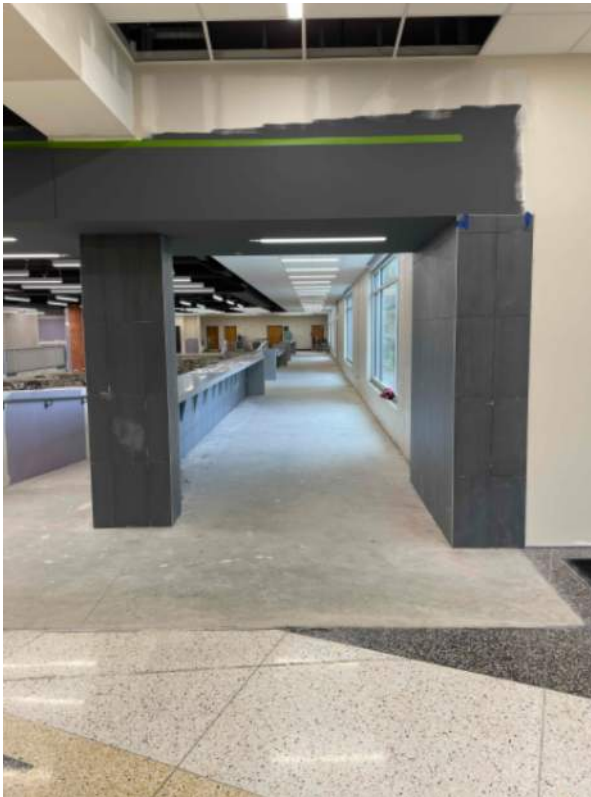High School – Commons wall tile.





	<p align="center">ICS Weekly Project Report October 25, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

Lake Ripley Elementary Interior Renovations

- **Completed Week ending Friday, October 22, 2021**
 - Continued commissioning of mechanical system
 - Training occurred for the controls and building automation system (BAS)
 - Installed back ordered paging speakers
 - Continued camera punch list items
 - Installed back ordered display case
 - Installed new handwashing station to replace cracked new one
- **Planned for Week ending Friday, October 29, 2021**
 - Continue commissioning of mechanical system

Middle School/High School Interior Renovations

- **Completed Week/ ending Friday, October 22, 2021**
 - Middle School
 - Contractors continued addressing punchlist items.
 - Completed inspections and turned-over Toilet and Locker Rooms.
 - Reception desk p-lam finish nearly complete.
 - Furniture installers assembled and placed backordered furniture pieces.
 - Media Center – continued hanging and finishing drywall.
 - Phase 2 Restrooms – Completed architectural demolition.
 - High School
 - Contractors continued addressing punchlist items.
 - Completed inspections and turned-over Toilet Rooms.
 - Reception desk p-lam finish nearly complete.
 - Continued Commons wall tile.
 - Furniture installers assembled and placed backordered furniture pieces
 - LVT flooring installed between gym and commons space
- **Planned for Week ending Friday, October 29, 2021**
 - Middle School
 - Media Center – continue drywall tape, mud and sand. Begin painting walls.
 - Phase 2 Restrooms – Complete plumbing, mechanical and electrical demolition.

	<p align="center">ICS Weekly Project Report October 25, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Furniture installers to continue assembling and placing backordered furniture pieces.
 -
- High School
 - Contractors to continue addressing punchlist items.
 - Continue Commons wall tile.
 - Continued installing backordered permanent doors and hardware.
 - Furniture installers to continue assembling and placing backordered furniture pieces.

Stadium Light Replacement .

- **Completed for Week ending Friday, October 22, 2021**
 - Musco submitted design and costs to ICS
- **Planned for Week ending Friday, October 29, 2021**
 - ICS to review and bring to POC design and costs



ICS Weekly Project Report
October 25, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley – Installed Hand Washing Station and Back Ordered Display Case






ICS Weekly Project Report
October 25, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Media Center drywall taping.

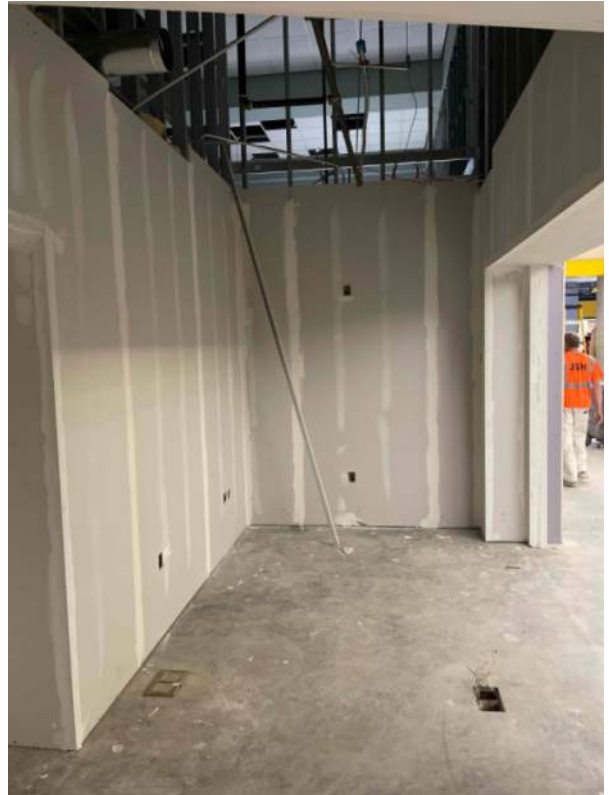



ICS Weekly Project Report
October 25, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Middle School – Restroom demolition progress.






ICS Weekly Project Report
October 25, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Reception desk plastic laminate finish.

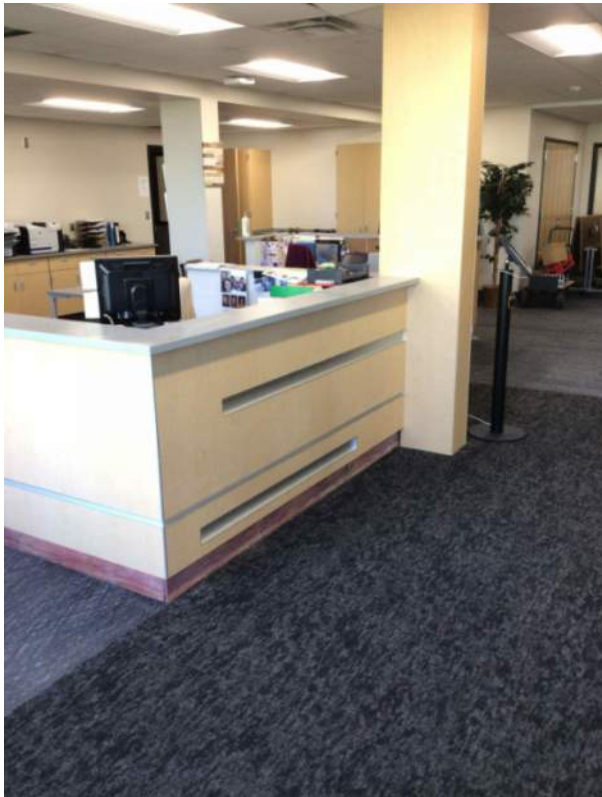



ICS Weekly Project Report
October 25, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

High School – Commons wall tile.

