


	<p align="center">ICS Weekly Project Report February 01, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, January 29, 2021**
 - POC meeting was held on 01/27/21
 - ICS/Wold presented bid authorization for Middle/High School project to School Board on 01/25/21
- **Planned for Week ending Friday, February 05, 2021**
 - Furniture group kick off meeting scheduled for 02/02/21

Lake Ripley Elementary

- **Completed Week/ ending Friday, January 29, 2021**
 - Kitchen/Cafeteria Addition
 - Continued exterior brick
 - Started roofing
 - Continued exterior window and metal panel framing
 - Continued overhead mechanical and electrical rough ins
 - Installed ground vapor barrier
 - Started to pour concrete floor slab
 - Main Entrance and Office Administration
 - Terminated data/electrical devices
 - Waiting for wall and floor tile to arrive
 - Waiting for interior glass to arrive
 - Continued flooring
 - Interior renovations Summer 2021/2022 work
 - Continued shop drawing review and approvals
- **Planned for Week ending Friday, February 05, 2021**
 - Kitchen/Cafeteria Addition
 - Continue exterior brick
 - Continue roofing
 - Continue exterior window and metal panel framing
 - Finish concrete floor slab
 - Main Entrance and Office Administration
 - Waiting for wall and floor tile to arrive next week

	<p align="center">ICS Weekly Project Report February 01, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Waiting for interior glass to arrive next week
- Interior renovations Summer 2021/2022 work
 - Continue reviewing shop drawings
 - Construction meeting scheduled for 02/04/2021
 - Met with Chris Olson to coordinate summer school planning

Middle School

- **Completed Week ending Friday, January 29, 2021**
 - Issued bid documents to contractors for pricing
- **Planned for Week ending Friday, February 05, 2021**
 - Issue addendum 1 bid documents
 - Meet with Principal Chelsea Brown to coordinate summer school planning

High School

- **Completed Week ending Friday, January 29, 2021**
 - Issued bid documents to contractors for pricing
- **Planned for Week ending Friday, February 05, 2021**
 - Issue addendum 1 bid documents



ICS Weekly Project Report
February 01, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Concrete Floor Pours





ICS Weekly Project Report
February 01, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Exterior Brick Progress







ICS Weekly Project Report
February 01, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Window Framing



	<p align="center">ICS Weekly Project Report February 08, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>



District Wide

- **Completed for Week ending Friday, February 05, 2021**
 - Furniture group kick off meeting held on 02/02/21
- **Planned for Week ending Friday, February 12, 2021**
 - POC meeting scheduled for 2/10/21

Lake Ripley Elementary

- **Completed Week/ ending Friday, February 05, 2021**
 - Kitchen/Cafeteria Addition
 - Continued exterior brick
 - Continued roofing
 - Continued exterior window and metal panel framing
 - Finished concrete floor slab
 - Started wall framing
 - Main Entrance and Office Administration
 - Floor/wall tile and interior glazing in transit
 - Interior renovations Summer 2021/2022 work
 - Continued shop drawing review and approvals
 - Construction meeting was held on 02/04/2021

- **Planned for Week ending Friday, February 12, 2021**
 - Kitchen/Cafeteria Addition
 - Continue exterior brick
 - Continue roofing
 - Continue mechanical and electrical rough ins
 - Continue wall framing
 - Rooftop HVAC unit to be delivered
 - Main Entrance and Office Administration
 - Install floor and wall tile in restroom
 - Install interior glass
 - Install bathroom plumbing fixtures
 - Final cleaning

	<p align="center">ICS Weekly Project Report February 08, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Interior renovations Summer 2021/2022 work
 - Continue reviewing shop drawings

Middle School

- **Completed Week ending Friday, February 05, 2021**
 - Met with Principal Chelsea Brown to coordinate summer school planning
 - Issued addendum 1 bid documents
- **Planned for Week ending Friday, February 12, 2021**
 - Issue addendum 2 bid documents
 - Pre-bid walkthrough with potential contractors 02/11/21

High School

- **Completed Week ending Friday, February 05, 2021**
 - Issued addendum 1 bid documents
- **Planned for Week ending Friday, February 12, 2021**
 - Issue addendum 2 bid documents
 - Pre-bid walkthrough with potential contractors 02/11/21
 - Meet with Principal Jason Michels to coordinate summer school planning




ICS Weekly Project Report
February 08, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Concrete Floor Patching

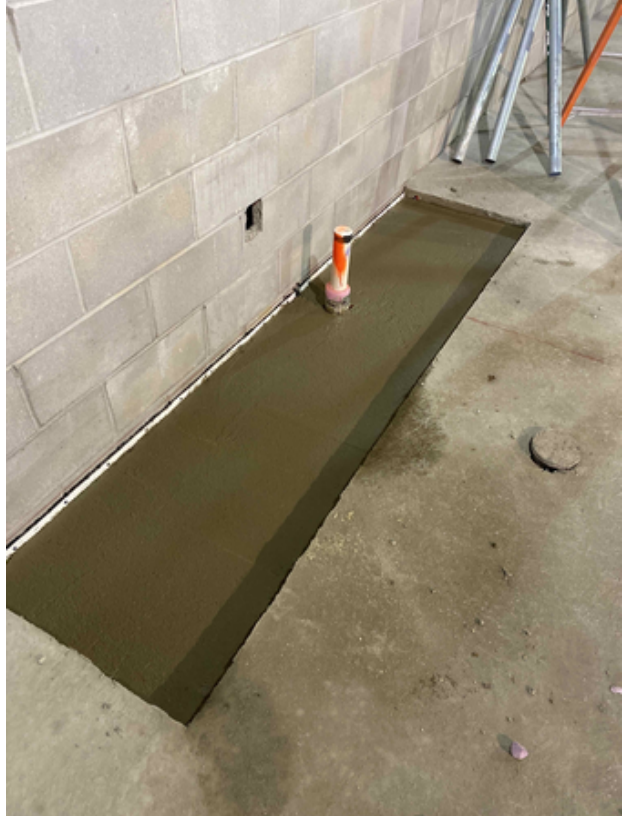



ICS Weekly Project Report
February 08, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Exterior Brick Progress





ICS Weekly Project Report
February 08, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Window Framing






ICS Weekly Project Report
February 08, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Wall Framing

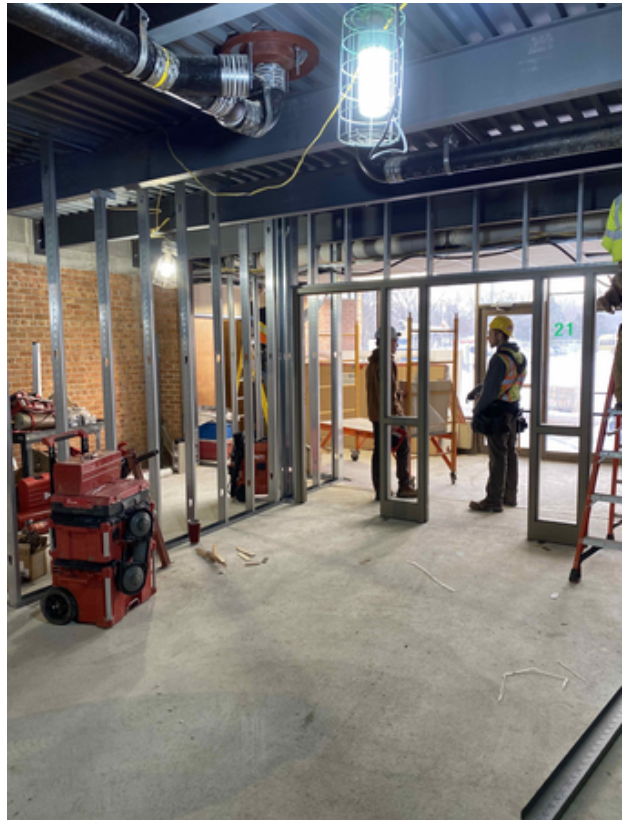





ICS Weekly Project Report
February 08, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Administration Space Progress





	<p align="center">ICS Weekly Project Report February 15, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, February 12, 2021**
 - POC meeting was held on 2/10/21
- **Planned for Week ending Friday, February 19, 2021**
 - Furniture user group meetings

Lake Ripley Elementary

- **Completed Week/ ending Friday, February 12, 2021**
 - Kitchen/Cafeteria Addition
 - Finished exterior brick
 - Continued roofing
 - Continued mechanical and electrical rough ins
 - Continued wall framing
 - Rooftop HVAC unit delivered
 - Main Entrance and Office Administration
 - Started installation floor and wall tile in restroom
 - Installed interior glass
 - Final cleaning
 - Interior renovations Summer 2021/2022 work
 - Continued shop drawing review and approvals
- **Planned for Week ending Friday, February 19, 2021**
 - Kitchen/Cafeteria Addition
 - Continue roofing
 - Continue mechanical and electrical rough ins
 - Continue wall framing
 - Main Entrance and Office Administration
 - Finish installation floor and wall tile in restroom
 - Install bathroom plumbing fixtures
 - Final cleaning
 - Install technology (wireless access points, card readers)
 - Punchlist
 - Interior renovations Summer 2021/2022 work

	ICS Weekly Project Report February 15, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

- Continue reviewing shop drawings
- Construction meeting scheduled for 02/18/21

Middle School

- **Completed Week ending Friday, February 12, 2021**
 - Issued addendum 2 bid documents
 - Pre-bid walkthrough with potential contractors was held on 02/11/21
- **Planned for Week ending Friday, February 19, 2021**
 - Issue addendum 3 bid documents

High School

- **Completed Week ending Friday, February 12, 2021**
 - Issued addendum 2 bid documents
 - Pre-bid walkthrough with potential contractors was held on 02/11/21
- **Planned for Week ending Friday, February 19, 2021**
 - Issue addendum 3 bid documents



ICS Weekly Project Report
February 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Window Framing





ICS Weekly Project Report
February 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Exterior Brickwork and Wall Framing








ICS Weekly Project Report
February 15, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

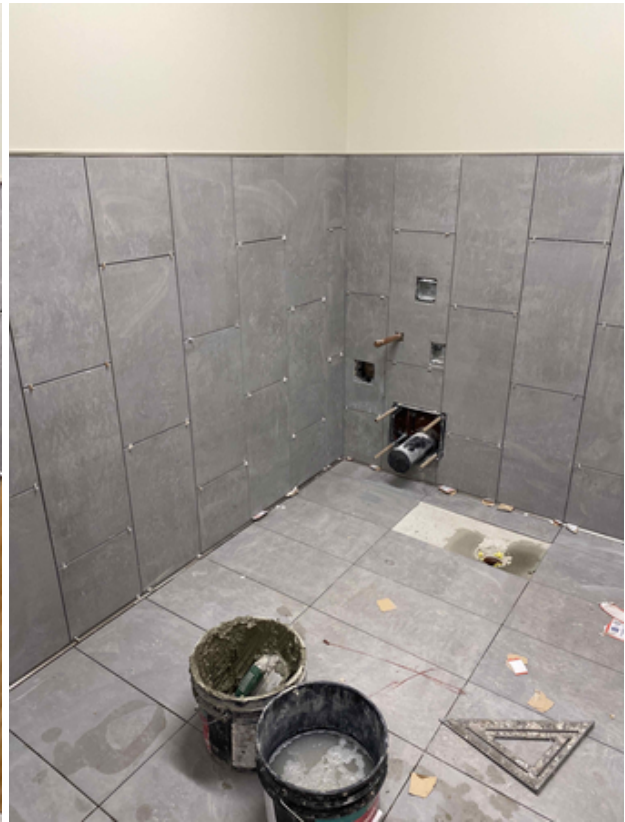Lake Ripley Administration Nurse Restroom Tile Work





	<p align="center">ICS Weekly Project Report February 22, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, February 19, 2021**
 - Furniture user group meetings held
- **Planned for Week ending Friday, February 26, 2021**
 - POC meeting scheduled for 2/24/21

Lake Ripley Elementary

- **Completed Week/ ending Friday, February 19, 2021**
 - Kitchen/Cafeteria Addition
 - Continued roofing
 - Continued mechanical and electrical rough ins
 - Continued wall framing
 - Main Entrance and Office Administration
 - Finished installation floor and wall tile in restroom
 - Installed bathroom plumbing fixtures
 - Final cleaning
 - Installed technology (wireless access points, card readers)
 - Punchlist
 - Interior renovations Summer 2021/2022 work
 - Continued reviewing shop drawings
 - Construction meeting was held 02/18/21
- **Planned for Week ending Friday, February 26, 2021**
 - Kitchen/Cafeteria Addition
 - Continue roofing
 - Continue mechanical and electrical rough ins
 - Finish wall and soffit framing
 - Install wall backing and start drywall work
 - Main Entrance and Office Administration
 - Receive occupancy and approval to start moving
 - Punch list work (signage, interior glass)
 - Testing, balancing, and commissioning of HVAC system
 - Interior renovations Summer 2021/2022 work

	<p align="center">ICS Weekly Project Report February 22, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Continue reviewing shop drawings
- Construction meeting scheduled for 02/25/21 to review Spring Break abatement and construction start in old/existing Administration area

Middle School

- **Completed Week ending Friday, February 19, 2021**
 - Issued addendum 3 and 4 bid documents
- **Planned for Week ending Friday, February 26, 2021**
 - Open bids 02/23/21

High School

- **Completed Week ending Friday, February 19, 2021**
 - Issued addendum 3 and 4 bid documents
 - Abatement coordination walkthrough
- **Planned for Week ending Friday, February 26, 2021**
 - Open bids 02/23/21



ICS Weekly Project Report
February 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Window and Soffit Framing





ICS Weekly Project Report
February 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Wall Framing and Mechanical Rough Ins





ICS Weekly Project Report
February 22, 2021



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Administration Nurse Restroom Plumbing Fixtures and Tile Work

