


	<b>ICS Weekly Project Report</b> September 7, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

### **Lake Ripley Elementary**

- **Completed Week ending Friday, September 3, 2021**
  - Installed ceiling in staff collaboration, staff bathroom/privacy room
  - Installed casework in staff collaboration room
  - Controls and condensing unit installation of HVAC system
  - Install casework in staff collaboration room
  - Vinyl floor and base patching
  - Cleared out south half of gymnasium and cleaned
  - Finish sinks in classrooms
  - Punch list and final cleaning
  
- **Planned for Week ending Friday, September 10, 2021**
  - Continue controls and condensing unit installation of HVAC system
  - Flooring in staff collaboration room
  - Finish lockers in corridors
  - Clear out north half of gymnasium and clean for use
  - Punch list

	<p align="center"><b>ICS Weekly Project Report</b> September 7, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Middle School/High School**

- **Completed Week/ ending Friday, September 3, 2021**
  - Middle School
    - Began tile work in the Special Ed. toilet room.
    - Continued installing door hardware.
    - Continued installing flooring and wall base.
    - Aluminum storefront entrances at the Main Entry/Admin Space is nearing completion.
    - Glass installation in hollow metal frames nearing completion.
    - Conducted architectural punch list walkthrough.
  - High School
    - Completed curb framing and sheathing at rooftop mech units. Started roofing tie-ins.
    - Glass installation in doors and hollow metal frames is nearing completion.
    - Started aluminum storefront entrances at the Main Entry/Admin space.
    - Continued miscellaneous painting throughout.
    - Continued wall and soffit framing in the Commons.
    - Continued overhead mechanical and electrical rough-in in the Commons.
    - Passed final inspection to allow full occupancy of the Admin. space.
- **Planned for Week ending Friday, September 7, 2021**
  - Middle School
    - Continue flooring and wall base.
    - Continue tile installation in the Toilet/Shower room and Locker Rooms.
    - Contractors to begin addressing punch list items.
  - High School
    - Complete floor prep and flooring installation in the Admin. space.
    - Continue Admin./Reception countertops and p-lam finishes.
    - Continue aluminum storefront framing and glass installation at the Lobby/Reception area.
    - Continue soffit and wall framing in the Commons.
    - Continued drywall hanging, taping, and finishing in the Commons.
    - Complete aluminum window frame and glass installation in the Commons.



ICS Weekly Project Report  
September 7, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley – Staff Collaboration Space





ICS Weekly Project Report  
September 7, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley – Staff Collaboration Space**





ICS Weekly Project Report  
September 7, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Reception area. Main Entry aluminum storefront framing in-progress.**





ICS Weekly Project Report  
September 7, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School –Interior hollow metal frame sidelight glass installed.**







ICS Weekly Project Report  
September 7, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Rooftop mechanical unit curbs framed and roofing tie-in in progress.**





ICS Weekly Project Report  
September 7, 2021





ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Commons area soffit framing and drywall.**







	<b>ICS Weekly Project Report</b> September 13, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

### **Lake Ripley Elementary**

- **Completed Week ending Friday, September 10, 2021**
  - Controls and condensing unit installation of HVAC system
  - Installed VCT flooring staff collaboration room
  - Finished lockers in corridors
  - Cleared out north half of gymnasium and clean for use
  - Installed ductwork in old cafeteria/new multipurpose room
  - Punch list
  
- **Planned for Week ending Friday, September 17, 2021**
  - Continue punch list
  - Finish connecting condensing units, start up and training on condensing units.
  - Paint ductwork and wall patches in old cafeteria/new multipurpose room
  - Clear out and start removing floor protection in old cafeteria/new multipurpose room
  - Training on air handling units

	<p align="center"><b>ICS Weekly Project Report</b> September 13, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Middle School/High School**

- **Completed Week/ ending Friday, September 10, 2021**
  - Middle School
    - Continued tile work in the Special Ed. Toilet/Shower room.
    - Continued flooring and wall base.
  - High School
    - Completed carpet and vinyl flooring in the Admin. space.
    - Continued overhead mechanical and electrical rough-in in the Commons.
    - Continued framing walls and soffits in the Commons.
    - Continued drywall hanging, taping and sanding in the Commons.
    - Began prepping for tile work in the Special Ed. Toilet/Shower rooms.
- **Planned for Week ending Friday, September 17, 2021**
  - Middle School
    - Complete remaining aluminum storefront framing and glass at the Main Entrance.
    - Continue installing wall base and flooring transitions.
    - Complete tile work in the Special Ed. Toilet/Shower room.
    - Heartland Business Systems to begin installing security cameras.
  - High School
    - Complete remaining aluminum storefront framing and glass at the Main Entrance.
    - Complete Commons aluminum windows and glass.
    - Complete framing, drywall and drywall taping/sanding in the Commons.
    - Complete painting of soffits and exposed structure in the Commons.
    - Complete decorative steel guardrails and handrails in the Commons.
    - Conduct inspections for student/staff occupancy of the Commons area.
    - Heartland Business Systems to begin installing security cameras.




ICS Weekly Project Report  
September 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley – Staff Collaboration Flooring Installed

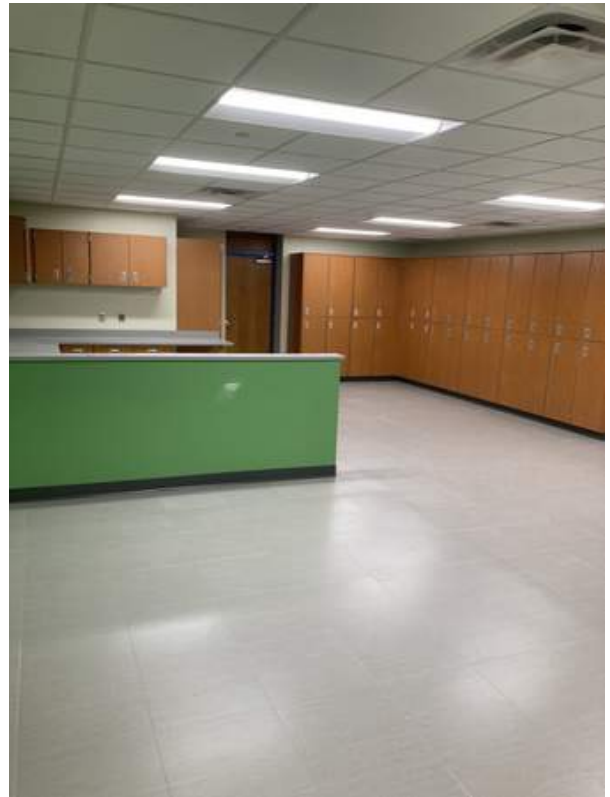



ICS Weekly Project Report  
September 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

### Lake Ripley – Old Cafeteria/New Multipurpose Room Ductwork Installation





ICS Weekly Project Report  
September 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Special Ed. tile work in-progress.**







**ICS Weekly Project Report**  
September 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Flooring installed throughout the Admin. space.**







**ICS Weekly Project Report**  
September 13, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum



**High School – Commons wall/soffit framing and drywall.**



	<b>ICS Weekly Project Report</b> September 20, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

### **Lake Ripley Elementary**

- **Completed Week ending Friday, September 17, 2021**
  - Continued punch list
  - Finished connecting condensing units, started up and trained on condensing units.
  - Painted ductwork and wall patches in old cafeteria/new multipurpose room
  - Cleared out and removed floor protection in old cafeteria/new multipurpose room
  - Training on air handling units
  - Camera installation
  
- **Planned for Week ending Friday, September 24, 2021**
  - Continue punch list
  - Camera terminations and programming
  - Continue programming and graphics on building automation system (BAS) interface
  - Remove all building materials out of old cafeteria/new multipurpose room

	<p align="center"><b>ICS Weekly Project Report</b> September 20, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

## **Middle School/High School**

- **Completed Week/ ending Friday, September 17, 2021**
  - Middle School
    - Aluminum storefront framing and glass at the Main Entrance is nearing completion.
    - Continued installing wall base and flooring transitions.
    - Completed walk-off carpet tile in the Vestibule/Reception space.
    - Tile work in the Special Ed. Toilet/Shower room nearing completion.
    - Heartland Business Systems to started installing security cameras.
  - High School
    - Aluminum storefront framing and glass at the Main Entrance is nearing completion.
    - Completed Commons aluminum windows and glass.
    - Framing, drywall and drywall taping/sanding in the Commons is nearing completion.
    - Continued painting of soffits and exposed structure in the Commons.
    - Completed decorative steel guardrails and handrails in the Commons.
    - Conducted inspections for student/staff occupancy of the Commons area.
    - Heartland Business Systems began installing security cameras.
- **Planned for Week ending Friday, September 24, 2021**
  - Middle School
    - Install plumbing fixtures and acoustical ceilings in the Special Ed. Toilet/Shower room.
    - Continue tile work in the Locker Rooms.
    - Continued installing wall base and flooring transitions.
    - Begin demolition in the Media Center.
  - High School
    - Continue painting walls and soffits in the Commons.
    - Apply concrete sealer in the Lower Commons.
    - Mount and begin patching in data rack in the Commons.
    - Install Reception desk countertops and wall caps.
    - Continue tile work in the Special Ed. Toilet/Shower rooms.



**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

- Continued installing wall base and flooring transitions.





**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley – Old Cafeteria/New Multipurpose Room Floor Protection Removed**





**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley – Camera Installation**





**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Locker Room tile progress.**





**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Toilet/Shower Room tile.**








**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Commons area progress.**

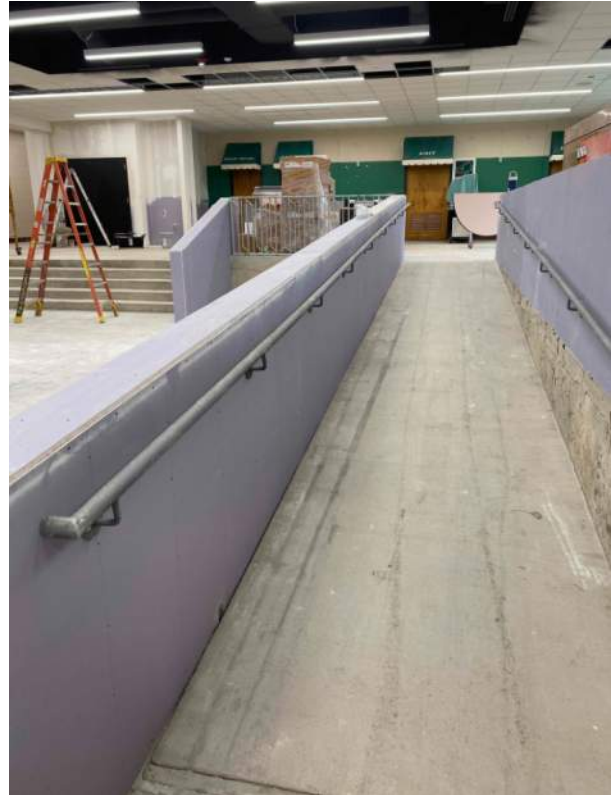





**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Toilet/Shower Room tile work.**








**ICS Weekly Project Report**  
September 20, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

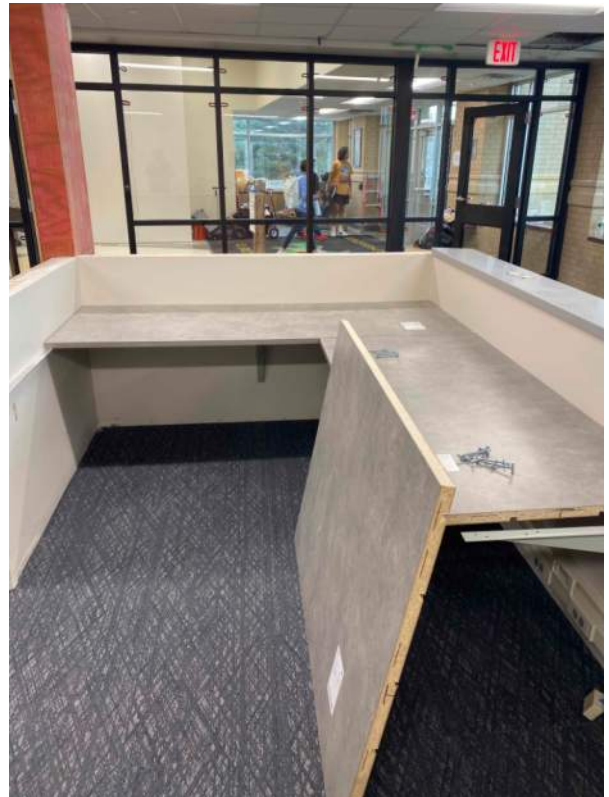

**High School – Reception desk countertops.**



	<b>ICS Weekly Project Report</b> September 27, 2021
	ISD #465 Litchfield Public Schools 2019 Referendum

### **Lake Ripley Elementary**

- **Completed Week ending Friday, September 24, 2021**
  - Continued punch list
  - Continued programming and graphics on building automation system (BAS) interface
  - Remove all building materials out of old cafeteria/new multipurpose room
  - Paging system (speaker) testing
  
- **Planned for Week ending Friday, October 1, 2021**
  - Continue punch list
  - Camera terminations and programming
  - Continue programming and graphics on building automation system (BAS) interface
  - Turn over old cafeteria/new multipurpose room for occupancy

	<p align="center"><b>ICS Weekly Project Report</b> September 27, 2021</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

### **Middle School/High School**

- **Completed Week/ ending Friday, September 24, 2021**
  - Middle School
    - Continued installing wall base and flooring transitions.
    - Completed tile work in the Special Ed. Toilet/Shower room.
    - Started installing fixtures in the Special Ed. Toilet/Shower room.
    - Continued installing tile in the Locker Rooms.
    - Demolition in the Media Center is nearing completion.
  - High School
    - Completed framing, drywall and tile backer board in the Commons.
    - Continued painting of soffits and exposed structure in the Commons.
    - Started solid surface tops and plastic laminate benches in the Commons.
    - Applied concrete sealer in the Lower Commons.
    - Complete Reception desk countertops.
    - Completed tile work in the Special Ed. Toilet/Shower room.
    - Started tile work in the Staff and Nurse Toilet Rooms.
- **Planned for Week ending Friday, October 1, 2021**
  - Middle School
    - Continue tile work in the Locker Rooms.
    - Complete plumbing fixtures and specialties in the Special Ed. Toilet/Shower room.
    - Continue installing wall base and flooring transitions.
    - Begin overhead mechanical and electrical rough-in in the Media Center.
  - High School
    - Complete painting walls and soffits in the Commons.
    - Mount and begin patching in data rack in the Commons.
    - Continued installing wall base and flooring transitions.
    - Continue solid surface tops and plastic laminate benches in the Commons.
    - Continue tile work in the Staff and Nurse Toilet Rooms.



**ICS Weekly Project Report**  
September 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Lake Ripley – Multipurpose Room Cleaned and Ready for Use**








**ICS Weekly Project Report**  
September 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Locker Room tile progress.**

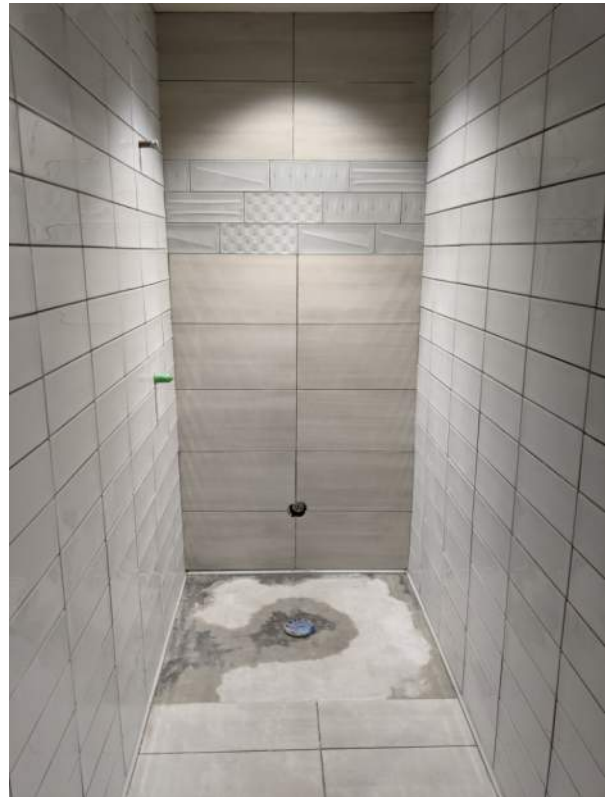




**ICS Weekly Project Report**  
September 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**Middle School – Media Center demolition progress.**

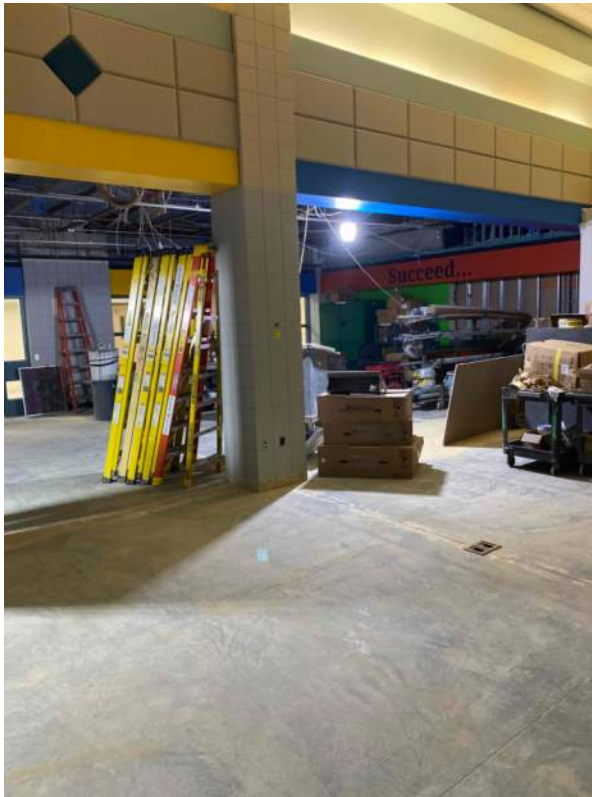



**ICS Weekly Project Report**  
September 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Commons area progress.**





**ICS Weekly Project Report**  
September 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Toilet/Shower Rooms tile work.**







**ICS Weekly Project Report**  
September 27, 2021



ISD #465 Litchfield Public Schools  
2019 Referendum

**High School – Staff and Nurse Toilet Room tile.**

