
	ICS Weekly Project Report November 02, 2020
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle School

- **Completed Week ending Friday, October 30, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 6, 2020**
 - Work on bid construction documents

High School

- **Completed Week ending Friday, October 30, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 6, 2020**
 - Work on bid construction documents





ICS Weekly Project Report
November 02, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Storage Concrete Slab Removal and Underground Utilities





	<p align="center">ICS Weekly Project Report November 02, 2020</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, October 30, 2020**
 - Presented to School Board the Construction Document Phase for the Middle School/High School on 10/26/20
- **Planned for Week ending Friday, November 6, 2020**
 - POC meeting scheduled for 11/04/20

Lake Ripley Elementary

- **Completed Week ending Friday, October 30, 2020,**
 - Kitchen/Cafeteria Addition
 - Construction meeting was held on 10/29/20
 - Additional underground locates
 - Site clearing and excavation for new utilities
 - Excavation and installation of underground fire main
 - Met with Innovative/SICO on a demonstration for cafeteria tables and chairs
 - Interior renovations Summer 2021/2022 work
 - Qualify bids and met with potential low responsible bidders
- **Planned for Week ending Friday, November 6, 2020**
 - Kitchen/Cafeteria Addition
 - Construction meeting scheduled for 11/05/20
 - Excavation for new utilities along with footings and foundations
 - Soil corrections
 - Main Entrance
 - Modify temporary construction walls and storefronts
 - Sawcut of concrete floors for underground plumbing
 - Site work construction
 - Punch list striping
 - West playground blacktop corrections
 - Interior renovations Summer 2021/2022 work
 - Continue to qualify bids and meet with potential low responsible bidders



	<p align="center">ICS Weekly Project Report November 09, 2020</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, November 6, 2020**
 - POC meeting was held on 11/04/20
- **Planned for Week ending Friday, November 13, 2020**
 - Present to School Board the recommendation to award to contractors on 11/9/20

Lake Ripley Elementary

- **Completed Week ending Friday, November 6, 2020,**
 - Kitchen/Cafeteria Addition
 - Construction meeting was held on 11/05/20
 - Excavation for new utilities along with footings and foundations
 - Soil corrections
 - Main Entrance
 - Modify temporary construction walls and storefronts
 - Sawcut of concrete floors for underground plumbing
 - Site work construction
 - Restriped visitor parking stalls
 - West playground blacktop corrections
 - Interior renovations Summer 2021/2022 work
 - Continued to qualify bids and meet with potential low responsible bidders
- **Planned for Week ending Friday, November 13, 2020**
 - Kitchen/Cafeteria Addition
 - Construction meeting scheduled for 11/12/20
 - Soil corrections
 - Main Entrance
 - Install underground plumbing
 - Pour back concrete floors
 - Start wall framing
 - Interior renovations Summer 2021/2022 work
 - Start execution of contracts with each work scope contractor
 - Review abatement contractor bids

	ICS Weekly Project Report November 09, 2020
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle School

- **Completed Week ending Friday, November 6, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 13, 2020**
 - Meet with staff on construction phasing and technology
 - Work on bid construction documents

High School

- **Completed Week ending Friday, November 6, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 13, 2020**
 - Meet with staff on construction phasing and technology
 - Work on bid construction documents



ICS Weekly Project Report
November 09, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Site Work Punch List (Striping and Playground Pavement Corrections)





Lake Ripley Kitchen Addition Excavation and Footings



Lake Ripley Main Entrance/Administration Saw Cutting/Underground Plumbing





	<p align="center">ICS Weekly Project Report November 16, 2020</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Completed for Week ending Friday, November 13, 2020**
 - ICS presented to School Board the recommendation to award to contractors on 11/9/20
- **Planned for Week ending Friday, November 20, 2020**
 - POC meeting is scheduled for 11/18/20

Lake Ripley Elementary

- **Completed Week ending Friday, November 13, 2020,**
 - Kitchen/Cafeteria Addition
 - Construction meeting was held 11/12/20
 - Soil testing due to potential contamination
 - Installed wood forms for concrete footings
 - Main Entrance
 - Installed underground plumbing
 - Poured back concrete floors
 - Started wall and door framing
 - Cut new openings through corridor
 - Interior renovations Summer 2021/2022 work
 - Started execution of contracts with each work scope contractor
 - Reviewed abatement contractor bids
- **Planned for Week ending Friday, November 20, 2020**
 - Kitchen/Cafeteria Addition
 - Construction meeting scheduled for 11/19/20
 - Soil corrections
 - Demonstration on cafeteria tables (Am Tab manufacturer) scheduled for 11/19/20
 - Pour concrete footings
 - Main Entrance
 - Continue wall and door framing
 - Continue mechanical and electrical rough ins

	<p align="center">ICS Weekly Project Report November 16, 2020</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Interior renovations Summer 2021/2022 work
 - Continue execution of contracts with each work scope contractor
 - Start submittal logs

Middle School

- **Completed Week ending Friday, November 13, 2020**
 - Met with staff on construction phasing and technology
 - User group meeting held for site work
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 20, 2020**
 - Work on bid construction documents

High School

- **Completed Week ending Friday, November 13, 2020**
 - Met with staff on construction phasing and technology
 - User group meeting held for site work
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 20, 2020**
 - Meet with staff on paint booth design
 - Work on bid construction documents



ICS Weekly Project Report
November 16, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Concrete Footings Formed





ICS Weekly Project Report
November 16, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Concrete Footings Formed



Lake Ripley Main Entrance/Administration Wall and Door Framing





ICS Weekly Project Report
November 16, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Main Entrance/Administration Wall and Door Framing





ICS Weekly Project Report

November 23, 2020





ISD #465 Litchfield Public Schools
2019 Referendum

District Wide

- **Completed for Week ending Friday, November 20, 2020**
 - POC meeting was held on 11/18/20
- **Planned for Week ending Friday, November 27, 2020**

Lake Ripley Elementary

- **Completed Week ending Friday, November 20, 2020,**
 - Kitchen/Cafeteria Addition
 - Construction meeting was held on 11/19/20
 - Soil corrections
 - Demonstration on cafeteria tables (Am Tab manufacturer) was held on 11/19/20
 - Poured concrete footings
 - Below grade masonry
 - Main Entrance
 - Continued wall and door framing
 - Continued mechanical and electrical rough ins
 - Cut in openings into corridor and for main entrance windows
 - Interior renovations Summer 2021/2022 work
 - Continued execution of contracts with each work scope contractor
 - Started submittal logs
- **Planned for Week ending Friday, November 27, 2020**
 - Kitchen/Cafeteria Addition
 - Remove unsuitable soils off site
 - Finish concrete footings
 - Finish below grade masonry include insulation
 - Backfill soils
 - Demo soffits in classrooms on adjacent common wall
 - Main Entrance
 - Continue mechanical and electrical rough ins
 - Wall backing and supports
 - Start drywall framing

	<p align="center">ICS Weekly Project Report November 23, 2020</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

- Interior renovations Summer 2021/2022 work
 - Continue execution of contracts with each work scope contractor
 - Continue submittal logs

Middle School

- **Completed Week ending Friday, November 20, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 27, 2020**
 - Work on bid construction documents

High School

- **Completed Week ending Friday, November 20, 2020**
 - Met with staff on paint booth design
 - Continued to work on construction documents
- **Planned for Week ending Friday, November 27, 2020**
 - Work on bid construction documents



ICS Weekly Project Report
November 23, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Below Grade Masonry





ICS Weekly Project Report
November 23, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Below Grade Masonry






ICS Weekly Project Report
November 23, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Main Entrance/Administration Openings

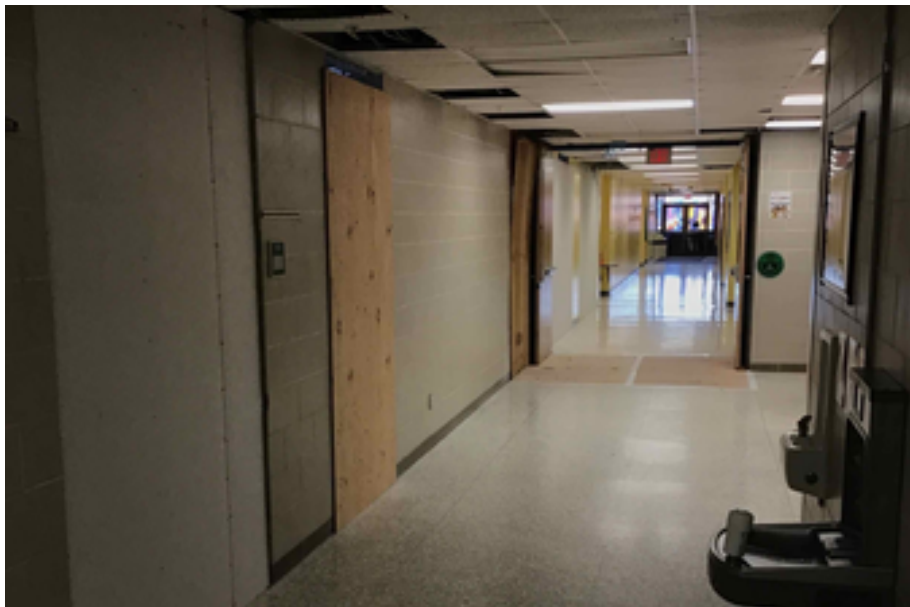





ICS Weekly Project Report
November 23, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Main Entrance/Administration Mechanical Rough Ins





	<p align="center">ICS Weekly Project Report November 30, 2020</p>
	<p align="center">ISD #465 Litchfield Public Schools 2019 Referendum</p>

District Wide

- **Planned for Week ending Friday, December 4, 2020**
 - POC meeting scheduled for 12/02/20

Lake Ripley Elementary

- **Completed Week ending Friday, November 27, 2020,**
 - Kitchen/Cafeteria Addition
 - Removed unsuitable soils off site
 - Finished concrete footings
 - Finish below grade masonry walls including insulation
 - Backfilled soils
 - Demolition of soffits in classrooms on adjacent common wall
 - Plumbing rough ins for hand washing fountains
 - Started above grade masonry walls
 - Main Entrance
 - Continued mechanical and electrical rough ins
 - Installed wall backing and supports
 - Started drywall framing
 - Interior renovations Summer 2021/2022 work
 - Continued execution of contracts with each work scope contractor
- **Planned for Week ending Friday, December 4, 2020**
 - Kitchen/Cafeteria Addition
 - .Continue above grade exterior masonry walls
 - Main Entrance
 - .Finish drywall installation
 - Start taping and mudding walls
 - Interior renovations Summer 2021/2022 work
 - Continue execution of contracts with each work scope contractor
 - Continue submittal logs

	ICS Weekly Project Report November 30, 2020
	ISD #465 Litchfield Public Schools 2019 Referendum

Middle School

- **Completed Week ending Friday, November 27, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, December 4, 2020**
 - Work on bid construction documents

High School

- **Completed Week ending Friday, November 27, 2020**
 - Continued to work on construction documents
- **Planned for Week ending Friday, December 4, 2020**
 - Work on bid construction documents



ICS Weekly Project Report
November 30, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Backfilled Soils





ICS Weekly Project Report
November 30, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Kitchen Addition Scaffolding for Above Grade Walls





ICS Weekly Project Report
November 30, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Main Entrance Drywall Installation





ICS Weekly Project Report
November 30, 2020



ISD #465 Litchfield Public Schools
2019 Referendum

Lake Ripley Main Entrance/Administration Openings into Corridor

